

**DOMINION BOULEVARD CONSTRUCTION
REPORT FOR
MARCH 2015**

Posted 4-21-15

Dominion Boulevard Improvements

AC # 01-6004-05

UPC: 56187

**VDOT Project No: (FO) 6017-131-109, PE-101, RW-201,
C-501, B608, B609, B610, B611, B614, B615, B616, D608,**

&

C-502, B612, B613

FHWA No.: HPP-0017-5(023)



New Bridge over Elizabeth River


Status Report as of March 25, 2015

TABLE OF CONTENTS

DESCRIPTION	PAGE NUMBER
1. PROJECT STATUS – Schedule and Budget	3
2. SIGNIFICANT ACCOMPLISHMENTS (03/01/15 to 03/31/15)	6
3. KEY OPERATIONS UNDERWAY	8
4. ANTICIPATED WORK (04/01/15 to 04/30/15)	11
5. CHANGE ORDERS AND QUANTITY OVERRUNS	12
6. RFI AND SUBMITTAL STATUS	15
7. SCHEDULE MILESTONES	16
ATTACHMENT: Progress Photographs	


PROJECT STATUS (Schedule and Budget)

Schedule		Budget	
Contract Type	Fixed Date	Original Contract Value	\$ 188,070,320
Fixed Contract Completion Date	04/01/2017	Exposure (Pending Change Orders)	\$ 918,277
Contract Duration (Days)	1,546	Expenditures (Approved Change Orders)	\$ 6,570,917
Time Extension (Days)	0	Exposure (Projected Quantity Overruns)	\$ 1,354,534
Current Contract Duration (Days)	1,546	Expenditures (Actual Quantity Overruns)	\$ 9,171,862
		11/26/13 Council Resolution-Scope Mod	\$ 3,000,000
Notice to Proceed	01/07/2013	Current Estimated Contract Value	\$ 209,085,910
First Day of Work	01/07/2013	Amount Paid Prior Periods	\$ 129,730,640
Contract Days Elapsed	814	Amount Paid this Period	\$ 2,336,496
Contract Days Remaining	732	Cumulative Amount Paid	\$ 132,067,136
Estimated Completion Date	04/01/2017	Value Stock Piled Materials	\$ 10,714,162
		Total Contract Cost to Date	\$ 142,781,298
% Contract Work Complete	56%		
% Contract Days Elapsed	53%	% Current Estimated Contract Value Paid (Not Including Stored Materials)	63%
% Contract Time Remaining	47%	% Current Estimated Contract Value Remaining	37%

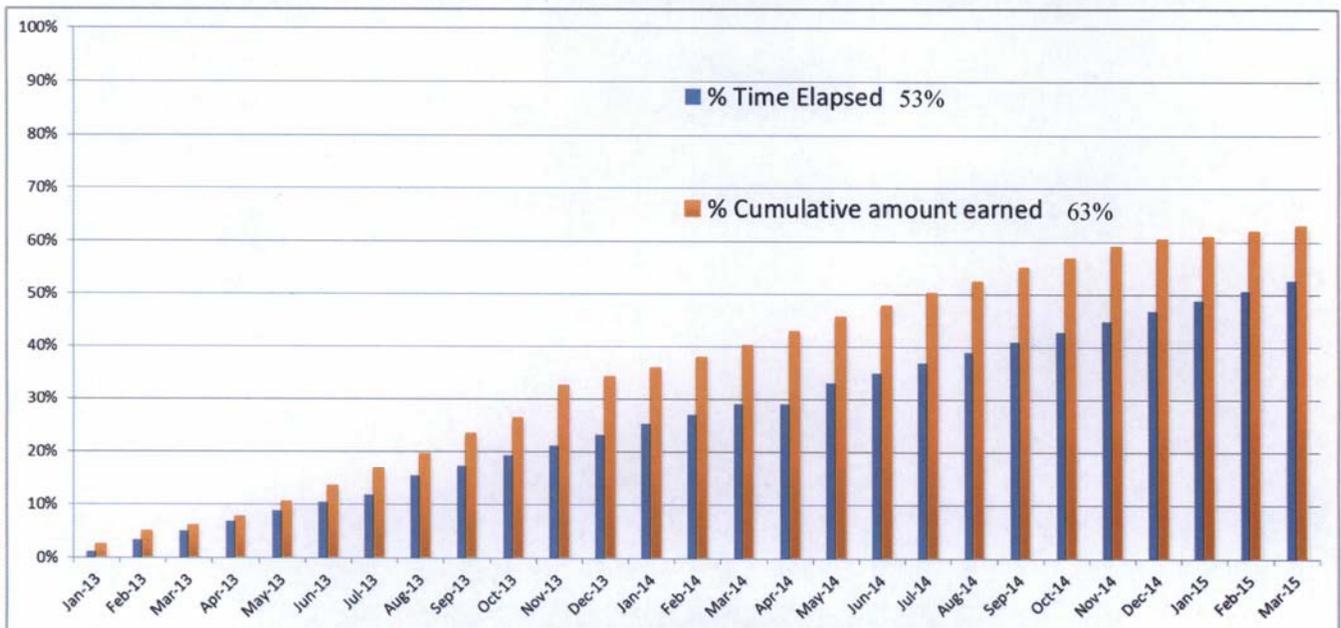


Cumulative amount paid vs Time Elapsed (NTP to March 31, 2015)

SCHEDULE Actual Percent Work Completed vs. Planned Percent Completed (All Activities)

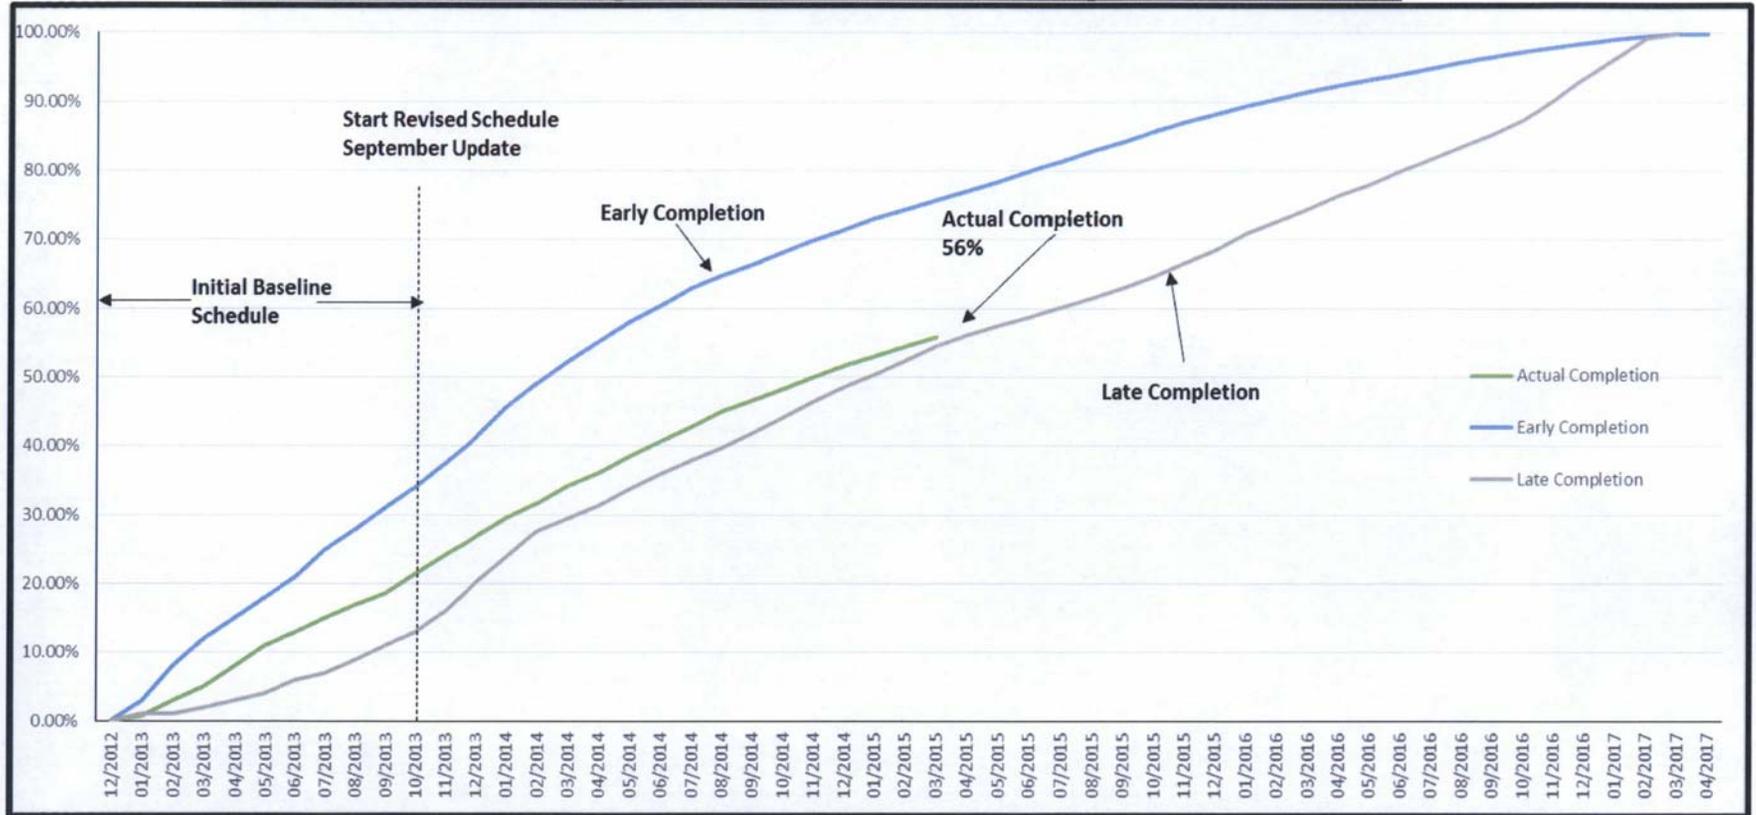


As of March 31, 2015

BUDGET
Actual Contract Cost to Date vs. Planned Contract Cost to Date

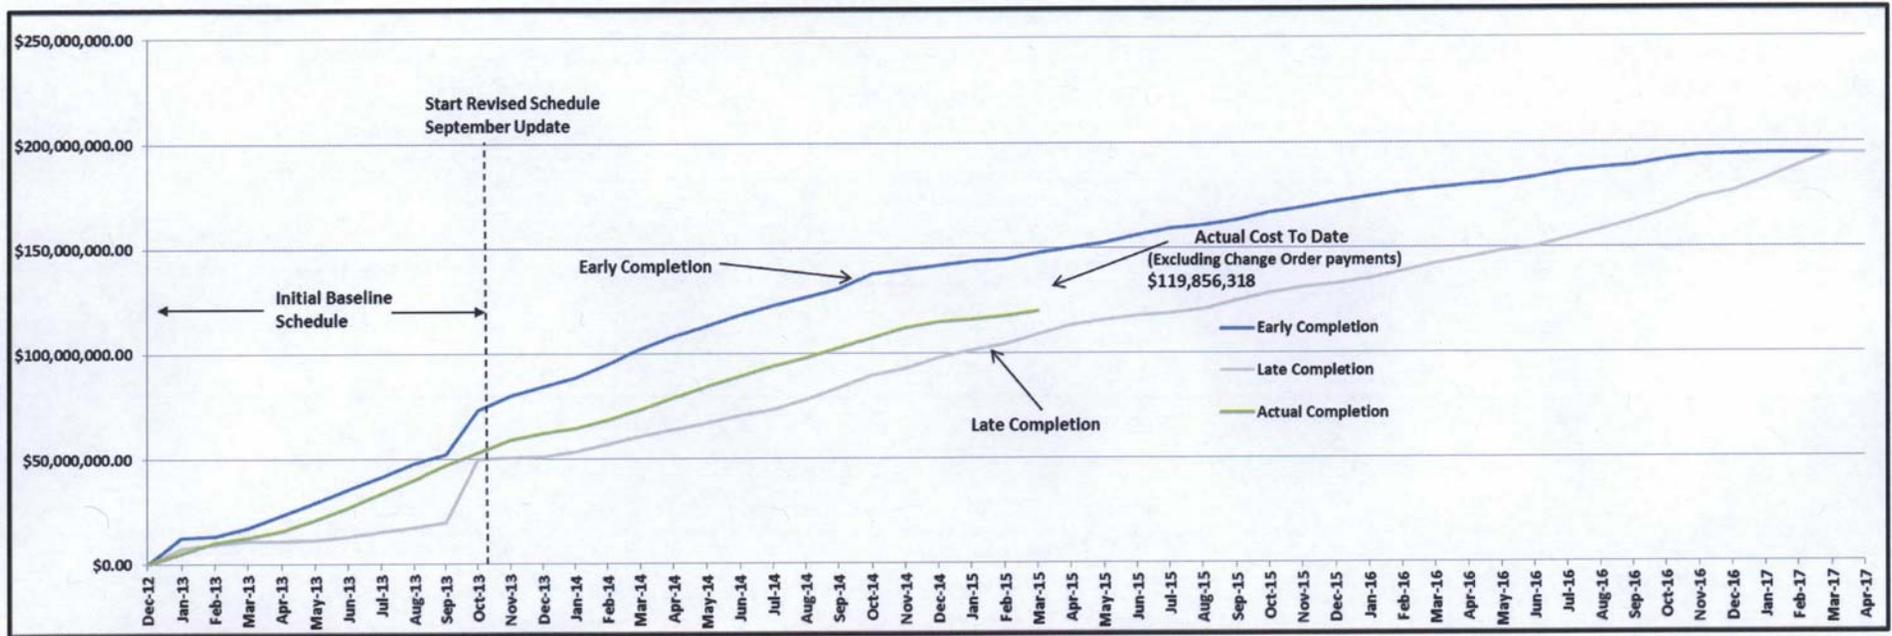

As of March 31, 2015

SIGNIFICANT ACCOMPLISHMENTS THIS MONTH (Mar. 1–Mar. 31, 2015)

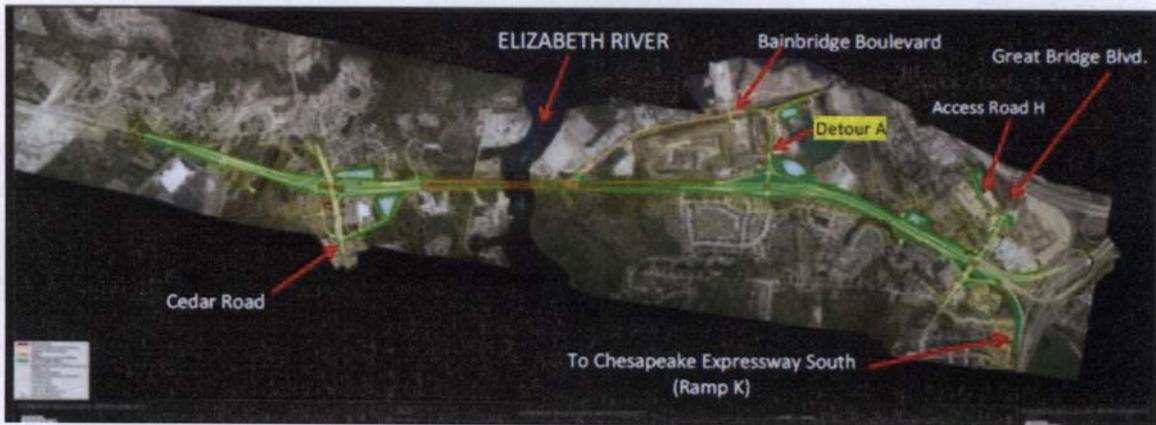

Bridge Descriptions	
	B612- Dominion Blvd SB over Cedar Rd/Moses Grandy Trail
B608- Dominion Blvd SB over Elizabeth River	B613- Dominion Blvd NB over Cedar Rd/Moses Grandy
B609- Dominion Blvd NB over Elizabeth River	B614- Dominion Blvd SB over Great Bridge Blvd
B610- Dominion Blvd SB over relocated Bainbridge Blvd	B615- Dominion Blvd NB over Great Bridge Blvd
B611- Dominion Blvd NB over Dominion Lakes Blvd/Relocated Bainbridge Blvd.	B616- Dom. Blvd./Rte. 168 SB Ramp over Great Bridge Blvd. to I-64 Ramp

Prime Contractor

DBC Joint Venture: (McLean Contracting Co, RR Dawson Bridge Co, Bryant Contracting Inc. and EV Williams Inc.)

Bridge Construction:

B609 (Dominion Blvd NB over Elizabeth River) – 100% Complete:

- Substantially completed Bridge B609 on 12/15/2014
- (See Attached Progress Photos)

B608 (Dominion Blvd SB over Elizabeth River) – Approximately 57% Complete:

- Continued driving production piles
- Continued placing concrete for pier caps and columns
- Began preparation for placing concrete for bridge deck

B616 (Dom. Blvd./Rte. 168 SB Ramp over Great Bridge Blvd. to I-64 Ramp) 100% Complete:

- Substantially completed Bridge B616 on 9/29/2014

B610 and B611 (Dominion Blvd SB and NB over relocated Bainbridge Blvd) – 100% Complete:

- Opened B611 for traffic on 12/15/2014

- Substantially completed Bridge B610 on 12/15/2014

B612 and B613 (Dominion Blvd SB and NB over Cedar Rd/Moses Grandy) - Approximately 45% Complete:

- Continued placing concrete for pier caps and columns

B614 and B615 (Dominion Blvd SB and NB over Great Bridge Blvd.) - Approximately 10% Complete


- Continued driving production piles

Roadway Construction (DBC, Inc):

- Continued installation of storm drainage system at various locations
- Continued monitoring advanced settlement from embankment surcharges, completed at several locations.
- Continued construction of ramps at the north and south ends of the project

Major Subcontractors

- **Bisette Construction Corp**
 - Continued installation of storm drain systems south of Elizabeth River at various locations along Cedar Road/Moses Grandy
- **Virginia Sign and Lighting**
 - Continued installing lighting conduits, poles and controls
- **Virginia Paving Co**
 - Began milling operations on Great Bridge Blvd.
- **Reliance Concrete Contractors**
 - Continued placing concrete for sidewalks and curb along Great Bridge Blvd
- **Lasting Coastline Inc**
 - Not on site

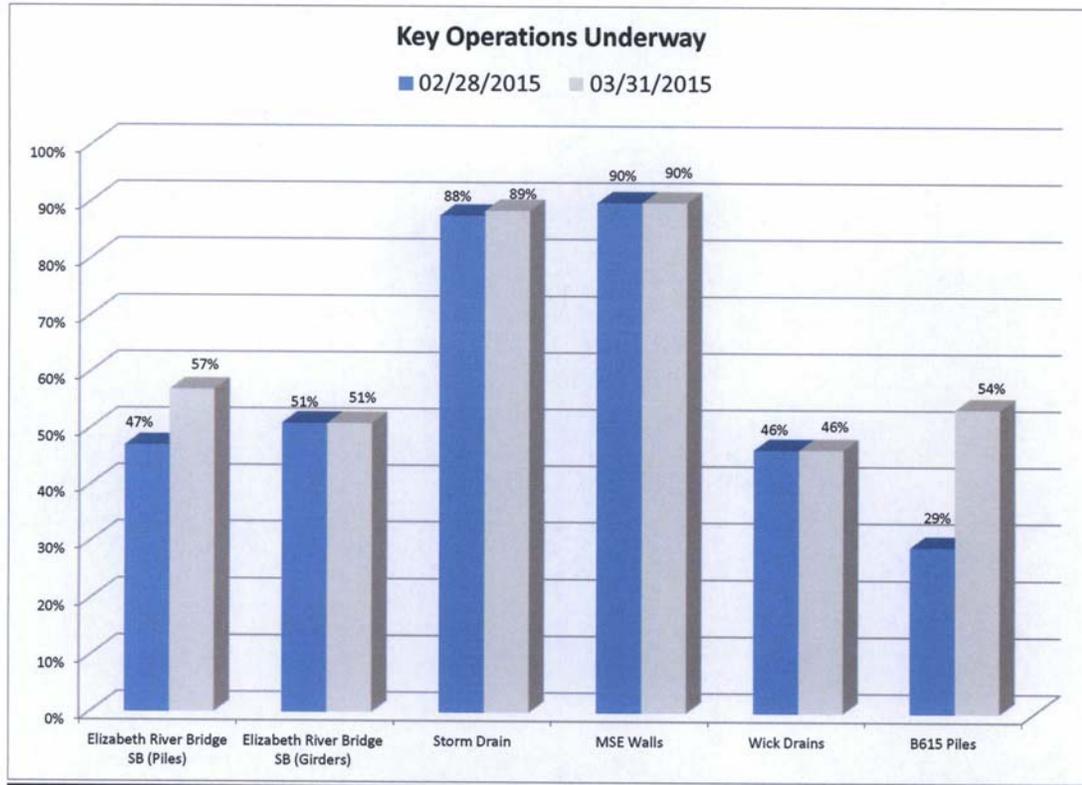


Project Key Operation Status as of 3/31/2015

Key Operations Completed	Month Completed
Elizabeth River Bridge NB (Bent Caps)	Aug-13
Elizabeth River Bridge NB (Piles)	Sep-13
Open Detour A	Oct-13
Elizabeth River Bridge NB (River Footings)	Nov-13
Opened relocated Dom Blvd. at Cedar Road	Jan-14
Partially opened Access A and Access AA	Mar-14
Opened Blake Street	Apr-14
Completed Setting Navigation Span Beams	May-14
Opened permanent intersection for Access A/AA at Cedar Rd.	Jun-14
Completed Stage 1 Post-Tensioning for B609 spliced Girders	Jul-14
Completed Dominion Lakes Blvd. entrance	Aug-14
Completed Driving Piles at B610 and B611	Aug-14
Completed Soil Nail Wall construction	Sep-14
Completed B609 Spliced Girder Post Tensioning	Oct-14
Completed Bridge decks for B609	Nov-14
Opened B609 and B611 on Dec. 15 th	Dec-14
Completed all Test Piles	Mar-15

MAINTENANCE OF TRAFFIC

Lane Closures

- Various temporary lane closures throughout project including night-time closures to minimize impacts to motorists
- Traffic on Dominion Blvd. remains shifted slightly to a temporary roadway at Moses Grandy to enable construction of B612 and B613 to begin. Sampson Creek Rd, Herberts Lane and Dominion Commons Way is open to traffic.

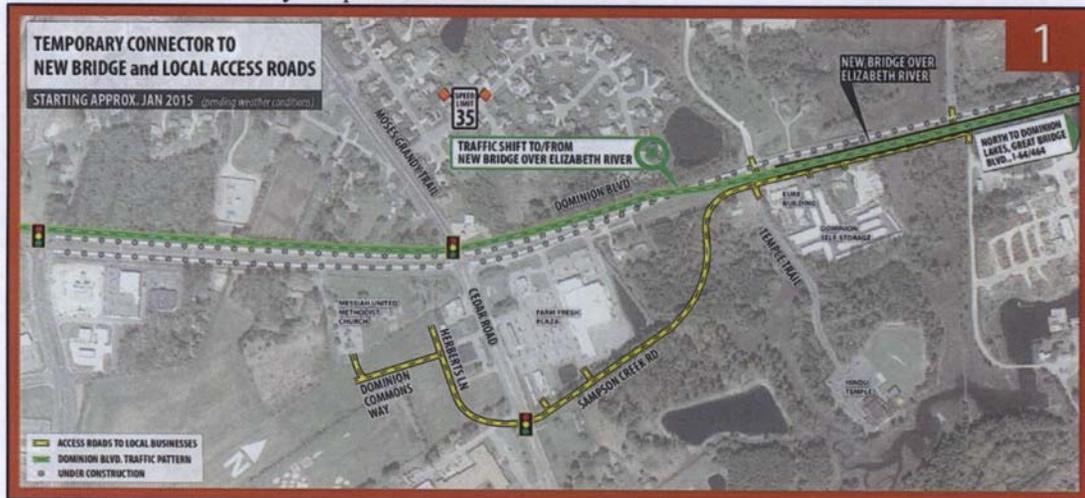

Traffic at Dominion Blvd/Cedar Rd Intersection

- Traffic on Dominion Blvd. shifted to the new bridge B609 over Elizabeth River. Traffic to Bainbridge Blvd. will enter through Great Bridge Blvd.




Traffic on B-609 over Elizabeth River:
(Arrows show traffic pattern for Dominion Blvd.)

- Traffic on Dominion Blvd has been shifted to the new bridge B-611 over Dominion Lakes. Dominion Lakes access to Bainbridge Blvd. is temporarily closed to traffic while the permanent connector is constructed.



**Traffic on B-611 over Dominion Lakes:
(Arrows show traffic pattern for Dominion Blvd.)**

- Traffic on Dominion Blvd. is temporarily shifted to the ramps to enable construction of the new Great Bridge Blvd Interchange.

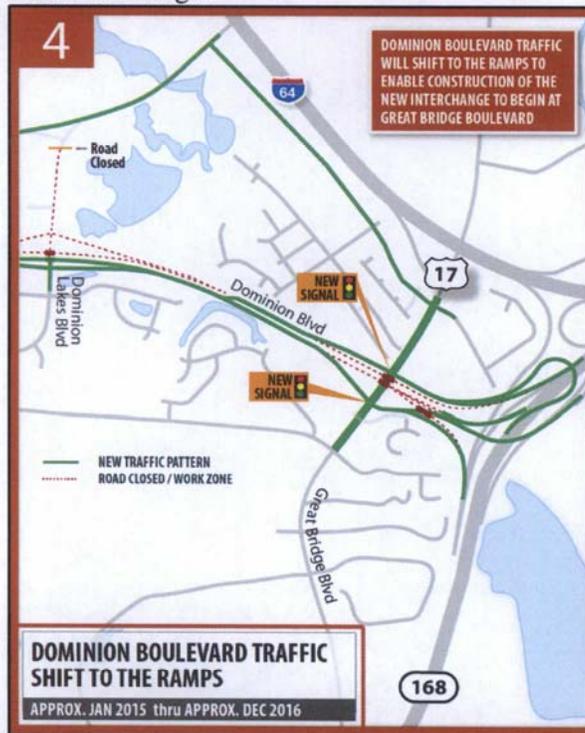

Traffic at Dominion Blvd./Great Bridge Blvd. Intersection

ANTICIPATED WORK PLANNED FOR NEXT MONTH (04/01/15 – 04/30/15)**DBC Joint Venture**

- B608 (Dominion Blvd. SB Bridge over Elizabeth River)
 - Install piles and concrete for river pier footings
 - Continue substructure construction north and south of the river
 - Continue placing deck concrete at north end of B608
- B612 and B613 (Dominion Blvd SB and NB over Cedar Rd/ Moses Grandy)
 - Continue preparations to erect girders
- B614 and B615 (Dominion Blvd SB and NB over Great Bridge Blvd.)
 - Continue driving piles and construction of substructure
- Demolition of the old Dominion Blvd. roadway
- Continue installation of storm drainage systems at various locations
- Roadway widening at Great Bridge Boulevard and Cedar Rd.

Roche Brothers

- Re-mobilize to continue construction of MSE Walls

Reliance Concrete Contractors Inc.

- Continue placing curb and gutter at various locations
- Continue concrete placement for moment slabs at various MSE Walls

Virginia Sign and Lighting

- Continue installing sign foundations at various locations
- Continued installing lighting conduits, poles and controls

Virginia Paving

- Continue widening of Great Bridge Blvd. and Cedar Road.

US Wick Drain

- Continue installing wick drains at various locations



Change Orders

Requested Change Orders

Change Order Number	Scope	Exposure from Change Orders (\$)	Expenditures from Change Orders (\$)
01	Add Flaggers & Portable Changeable Message Signs		\$91,071.25
02	Replace Porous fill with strip drains at MSE Walls		(\$1,444,802.94)
03	Raise B608 & B609 Bridge Footings		(\$810,117.50)
04	Add 1 electric service per plan Rev. 1/18/2013		\$139,651.02
05	Add #57 stone to the contract		\$851,600.00
06	Add Trainees to the contract		\$45,000.00
07	2" HDPE Conduit - Bored		\$25,747.68
08	8" Sanitary Force Main Under Wetlands		\$22,601.25
09	B609 Pier 14 Pile Modif.		\$831,940.75
10	Temp. Signal at Bainbridge and Sta. 55+50		\$73,977.55
11	Type D Removable Pavement Markings for Concrete		\$47,400.00
12	Removal of Concrete Barriers (\$12.50/LF)		\$6,000.00
13	Ramp K/MSE Wall 22 Wick Drains		\$305,633.61
14	Demolition/Removal of Existing Sound Wall		\$72,643.23
15	Disposal of Unsuitable Material (base on 140,000 cy)		\$6,025,600.00
16	MSE Walls at Bridge Abutments B610-B615		(\$239,207.30)
17	Delete Aesthetic Treatment		(\$1,838,302.58)
18	4 inch water meters at Great Bridge & Cedar		\$10,772.06
19	Relocation of the Pressure Sensor Telemetry Cabinet; 8/29/2013 Questions to DBC		\$23,457.35
20	Water Meter Vault at DR-1J50-1		\$11,157.98
21	Anti-Graffiti Paint - 8/26 Rec'd DBC's Revised Scope		\$219,823.36
22	16 inch Waterline Repairs at Bainbridge		\$18,116.70
23	Temp. Street lights at Cedar/Dominion Blvd		16,717.73
24	Soil Nail Wall		\$247,184.50
25	12" x 12" x 8" Junction Boxes		\$36,026.55
26	Installation of Leak Detectors Water/Sewer Casings		\$47,359.48
27	New High Mast Light Assembly		\$60,454.18
28	Grass Cutting		\$152,556.48
29	Missing Pay Items: RW2, RW3, Impact Attenuators		\$361,862.19
30	Replace MC-3B Asphalt Curb with Conc. Curb (VEP 07)		-\$39,402.03
31	Remove Existing Sign Structures		\$6,192.66
32	GPS As-Builts of Utilities		\$84,527.20
33	Plan Revision No. 14 Additional Work		\$476,877.44
34	Soil Nail Walls - Additional Work		\$141,766.40
35	Replace existing junction boxes		\$15,192.04
36	Wireless System Coaxial Cable for Traffic Signals		\$22,085.04
37	MSE Wall Redesign		\$318,630.21
38	Conflict Manhole at 4" Sanitary Force Main		\$8,095.62
39	CCW Type D Lighting Control Cabinets		\$125,028.30
40	Bored conduit for Utility Relocations at B614/B615	\$99,564.40	
41	Obstruction at 18" Jack and Bore	\$24,795.13	
42	VDOT VMS Sign Removal/Reinstall	\$66,935.33	
	VMS Conductor Cable (combined with CO 42 VMS Removal)		
43	VEP No. 9 MSE Wall i.l.o. RW-3 Wall (Credit)	(\$35,987.69)	
44	Temporary Drainage at Detour A	\$17,634.06	
45	Additional Restrained Waterline	\$10,793.22	
46	Obstructions between Str. 23N-1 and 23N-2	\$19,240.31	
47	Additional Work Associated with Revision 10	\$36,767.40	
48	24" Waterline tie-in delays at Cedar Road	\$16,731.79	
	Additional Cost 16" Waterline Tie-in at River (Combined with CO 48)		
49	Waterline Joint Restraint at Great Bridge Blvd.	\$4,701.38	
(TBD)	Structure 32-10 Add.	\$8,929.89	
(TBD)	Plan Rev. No. 8 8" PVC Sewer	\$16,808.21	
(TBD)	Removal of Underground Water Storage Tanks	\$15,065.49	
(TBD)	Installation of Verizon Vaults and Pedestals	\$64,255.85	
(TBD)	24" x 6" Reducer for Additional Fire Hydrant	\$4,172.63	
(TBD)	Connection of Existing Sewer Laterals to New, Relocated Sewer Main	\$18,061.62	
(TBD)	Plan Revision No 12 Added Wick Drains/Survey	\$35,593.37	
(TBD)	Remove/Salvage Existing Signal Equipment	\$39,115.32	
(TBD)	Plan Revision No. 13 Additional Work	\$19,456.14	
(TBD)	B609 Pier No. 3-8 Rebar Changes to Caps	\$21,753.35	
(TBD)	Plan Revision No. 15 Additional Work	\$29,528.83	
(TBD)	VPDES Permit Re-application and Maintenance Fee	\$16,054.35	
(TBD)	Optional Tolling Interoperability Functionality	\$310,626.13	
(TBD)	Remove Existing Sign Structures D704 & D14	\$8,214.60	
(TBD)	Mitigation Basin Goose Protection Fencing	\$49,466.53	
	TOTAL	\$918,277.64	\$6,570,917.46



Unit Price Item Quantities – Projected and Actual Overruns

Unit Price Item Quantity Overruns (Projected Quantity Overruns)					
Item Number	Description	Projected Quantity Overrun	Units	Unit Price	Projected Cost Overrun
111	CLEARING AND GRUBBING	28.16	AC	\$ 7,700.00	\$ 216,832.00
120	REGULAR EXCAVATION	38062	CY	\$ 29.00	\$ 1,103,798.00
212	MINOR STRUCTURE EXCAVATION BOX CULVERT	1280	CY	\$ 35.00	\$ 44,800.00
505	BEDDING MATERIAL AGGR. NO. 25 OR 26	2800	TON	\$ 78.50	\$ 219,800.00
27500	GEOTEXTILE FABRIC	24910	SY	\$ 6.70	\$ 166,897.00
525	CONCRETE CLASS A3 MISC.	84	CY	\$ 2,913.26	\$ 244,713.84
2192	30" X 19" ELLIPTICAL CONC. PIPE	341	LF	\$ 150.00	\$ 51,150.00
27550	STORMWATER MANAGEMENT DRAINAGE STRUCTURE SWM-1	23	LF	\$ 6,232.87	\$ 143,356.01
9148	EROSION CONTROL STONE (CLASS A1), EC-1	978	SY	\$ 111.98	\$ 109,516.44
9150	EROSION CONTROL STONE (CLASS I), EC-1	3610	SY	\$ 147.48	\$ 532,402.80
85003	UNDERCUT EXC @ TWICE REG EXC	35096.43	CY	\$ 50.00	\$ 1,754,821.50
10636	ASPHALT CONCRETE TY. SM-9.5D	1750	TON	\$ 75.00	\$ 131,250.00
10128	AGGR. BASE MATL. TY. I NO. 21B	9000	TON	\$ 28.23	\$ 254,070.00
10417	TACK COAT	1850	GAL	\$ 15.90	\$ 29,415.00
13487	MEDIAN BARRIER MB-8A TYPE III	348	LF	\$ 162.83	\$ 56,664.84
22643	FENCE FE-CL	3800	LF	\$ 12.19	\$ 46,322.00
24703	NS REMOVE EXIST. (PIPE)	1401	LF	\$ 25.94	\$ 36,341.94
9151	EROSION CONTROL STONE, EC-1 (STD. PG-3 TYPE I, CLASS I)	397	SY	\$ 83.27	\$ 33,058.19
27321	PROTECTIVE COVERING EC-2	84383	SY	\$ 1.35	\$ 113,917.05
13570	NS RETAINING WALL SOIL NAIL	626	SF	\$ 200.04	\$ 125,225.04
13570	NS RETAINING WALL TEMPORARY	12160	SF	\$ 30.00	\$ 364,800.00
2093	NS PRE-DRILLING OF WICK DRAINS	851250.725	LF	\$ 1.85	\$ 1,574,813.84
64808	DRIVING TEST FOR PRESTRESSED CONCRETE PILES 12"	1319	LF	\$ 55.00	\$ 72,545.00
515	TEMPORARY SHEET PILING	10000	SF	\$ 25.00	\$ 250,000.00
10065	AGGR. MATL. NO. 1	1000	TON	\$ 35.91	\$ 35,910.00
24283	POLICE PATROL	2200	HR	\$ 42.40	\$ 93,280.00
54550	CONSTR. PAVE. MARK. (TY. F, CL I) 4"	217800	LF	\$ 0.25	\$ 54,450.00
56052	BORED CONDUIT 4"	31580	LF	\$ 32.90	\$ 1,038,982.00
56053	2" PVC CONDUIT	36330	LF	\$ 2.25	\$ 81,742.50
56055	4" PVC CONDUIT	12393.04	LF	\$ 4.81	\$ 59,610.52
64416	PRESTR. CONCRETE PILES 16"	786	LF	\$ 65.00	\$ 51,090.00
61704	CORROSION RESISTANT REINF. STEEL (Plan Quantity)	17440.2	LB	\$ 2.00	\$ 34,880.40
64424	PRESTR. CONCRETE PILES 24"	400.6	LF	\$ 80.00	\$ 32,048.00
64868	DRIVING TEST FOR 24" PRESTR. CONC. PILE	237	LF	\$ 150.00	\$ 35,550.00
64416	PRESTR. CONCRETE PILES 16"	770.77	LF	\$ 65.00	\$ 50,100.05
40081	8" DI WATER MAIN	1220	LF	\$ 47.74	\$ 58,242.80
42080	8" PVC SAN PIPE	269.35	LF	\$ 157.15	\$ 42,328.35
41982	NS 4" OFFSET	6	EA	\$ 4,705.65	\$ 28,233.90
44301	NS FURNISH and INSTALL 24" LINSTOP	2	EA	\$ 73,658.52	\$ 147,317.04
38900	NS SALT MARSH CORDGRASS, 2" PLUG	20320	EA	\$ 1.95	\$ 39,624.00
42080	8" DI SAN PIPE	365	LF	\$ 93.51	\$ 34,131.15
	Miscellaneous				\$ 932,365.04
	Total				\$ 10,526,396.24


Summary Unit Price Item Overruns:

Current Projected Quantity Overruns	\$ 10,526,396.24
Actual Quantity Overruns	\$ 9,171,862.30
Net Projected Quantity Overruns	\$ 1,354,533.94




Unit Price Item Quantity Overruns (Actual Quantity Overruns)						
Item Number	Description	Actual Quantity Overrun	Units	Unit Price	Actual Cost Overrun	
111	CLEARING AND GRUBBING	28.16	AC	\$ 7,700.00	\$ 216,832.00	
120	REGULAR EXCAVATION	38048.2	CY	\$ 29.00	\$ 1,103,397.80	
	MINOR STRUCTURE EXCAVATION BOX CULVERT	1182.83	CY	\$ 35.00	\$ 41,399.05	
505	BEDDING MATERIAL AGGR. NO. 25 OR 26	2763.41	TON	\$ 78.50	\$ 216,927.69	
27500	GEOTEXTILE FABRIC	24424.98	SY	\$ 6.70	\$ 163,647.37	
525	CONCRETE CLASS A3 MISC.	76.55	CY	\$ 2,913.26	\$ 223,010.05	
1482	48" CONC. PIPE	100.9	LF	\$ 208.18	\$ 21,005.36	
2192	30" X 19" ELLIPTICAL CONC. PIPE	341	LF	\$ 150.00	\$ 51,150.00	
2292	45" X 29" ELLIPTICAL CONC. PIPE	48	LF	\$ 252.39	\$ 12,114.72	
27550	STORMWATER MANAGEMENT DRAINAGE	22.9	LF	\$ 6,232.87	\$ 142,732.72	
9056	MANHOLE MH-10R MH-2	18	LF	\$ 853.96	\$ 15,371.28	
9148	EROSION CONTROL STONE (CLASS A1), EC-1	814.29	SY	\$ 111.98	\$ 91,184.19	
9150	EROSION CONTROL STONE (CLASS I), EC-1	3580.05	SY	\$ 147.48	\$ 527,985.77	
85003	UNDERCUT EXC @ TWICE REG EXC	35086.5	CY	\$ 50.00	\$ 1,754,325.00	
10636	ASPHALT CONCRETE TY. SM-9.5D	145.1	TON	\$ 75.00	\$ 10,882.50	
10128	AGGR. BASE MATL. TY. I NO. 21B	4283.17	TON	\$ 28.23	\$ 120,913.89	
10417	TACK COAT	1830.56	GAL	\$ 15.90	\$ 29,105.90	
12940	ENTRANCE GUTTER CG-9D	155.38	SY	\$ 70.73	\$ 10,990.03	
13487	MEDIAN BARRIER MB-8A TYPE III	348	LF	\$ 162.83	\$ 56,664.84	
22643	FENCE FE-CL	1292	LF	\$ 12.19	\$ 15,749.48	
24602	REMOVE EXISTING (FENCE)	6771	LF	\$ 3.18	\$ 21,531.78	
51910	SAW CUT	9925	LF	\$ 2.07	\$ 20,544.75	
24703	NS REMOVE EXIST. (PIPE)	1025	LF	\$ 25.94	\$ 26,588.50	
9151	EROSION CONTROL STONE, EC-1 (STD. PG-3 TYPE	371.49	SY	\$ 83.27	\$ 30,933.97	
27321	PROTECTIVE COVERING EC-2	81677.05	SY	\$ 1.35	\$ 110,264.02	
13570	NS RETAINING WALL SOIL NAIL	626	SF	\$ 200.04	\$ 125,225.04	
13570	NS RETAINING WALL TEMPORARY	12082.3	SF	\$ 30.00	\$ 362,469.00	
2093	NS PRE-DRILLING OF WICK DRAINS	622209	LF	\$ 1.85	\$ 1,151,086.65	
64808	DRIVING TEST FOR PRESTRESSED CONCRETE PILES	749	LF	\$ 55.00	\$ 41,195.00	
27410	CHECK DAM, ROCK-TYPE I	31	EA	\$ 370.67	\$ 11,490.77	
27526	TURBIDITY CURTAIN, IMPERVIOUS	1226	LF	\$ 18.02	\$ 22,092.52	
515	TEMPORARY SHEET PILING	6806.43	SF	\$ 25.00	\$ 170,160.75	
10065	AGGR. MATL. NO. 1	425.0292	TON	\$ 35.91	\$ 15,262.80	
24283	POLICE PATROL	1292.34	HR	\$ 42.40	\$ 54,795.22	
54240	TEMP. PAVE. MARKER 1 WAY	2628	EA	\$ 7.95	\$ 20,892.60	
54550	CONSTR. PAVE. MARK. (TY. F, CL I) 4"	190728.27	LF	\$ 0.25	\$ 47,682.07	
56052	BORED CONDUIT 4"	29781	LF	\$ 32.90	\$ 979,794.90	
56053	2" PVC CONDUIT	15537	LF	\$ 2.25	\$ 34,958.25	
56055	4" PVC CONDUIT	6024	LF	\$ 4.81	\$ 28,975.44	
56200	TRENCH EXCAVATION ECI-1	2476	LF	\$ 4.59	\$ 11,364.84	
55588	IN-GRADE JUNCTION BOX (JB-S1, S2 OR S3)	10	EA	\$ 1,500.00	\$ 15,000.00	
64416	PRESTR. CONCRETE PILES 16"	707	LF	\$ 65.00	\$ 45,955.00	
536	NS CONCRETE CLASS A5, SPLICED GIRDER DECK, 5 K	24	CY	\$ 650.00	\$ 15,600.00	
61704	CORROSION RESISTANT REINF.STEEL (Plan Quantity	17439	LB	\$ 2.00	\$ 34,878.00	
64101	DYNAMIC PILE TEST (FRICTION PILES)	4.333	EA	\$ 3,000.00	\$ 12,999.00	
64416	PRESTR. CONCRETE PILES 16"	338	LF	\$ 65.00	\$ 21,970.00	
64424	PRESTR. CONCRETE PILES 24"	400.6	LF	\$ 80.00	\$ 32,048.00	
64868	DRIVING TEST FOR 24" PRESTR. CONC. PILE	237	LF	\$ 150.00	\$ 35,550.00	
60404	CONCRETE CLASS A4	24.6	CY	\$ 580.00	\$ 14,268.00	
60404	CONCRETE CLASS A4	25.7	CY	\$ 580.00	\$ 14,906.00	
64101	DYNAMIC PILE TEST (FRICTION PILES)	3.333	EA	\$ 5,000.00	\$ 16,665.00	
64416	PRESTR. CONCRETE PILES 16"	335	LF	\$ 60.00	\$ 20,100.00	
66921	NS BRIDGE SUB-STRUCTURE PRE-BORING (16"	460	LF	\$ 25.00	\$ 11,500.00	
64416	PRESTR. CONCRETE PILES 16"	491	LF	\$ 65.00	\$ 31,915.00	
61704	CORROSION RESISTANT REINF.STEEL (Plan	5690	LB	\$ 1.80	\$ 10,242.00	
40061	6" DI WATER MAIN	483	LF	\$ 42.31	\$ 20,435.73	
40081	8" DI WATER MAIN	753.84	LF	\$ 47.74	\$ 35,988.32	
40121	12" DI WATER MAIN	202	LF	\$ 83.54	\$ 16,875.08	
40161	16" DI WATER MAIN	147	LF	\$ 86.80	\$ 12,759.60	
40408	18" BEND	4	EA	\$ 2,820.91	\$ 11,283.64	
40992	NS 8" BEND	26	EA	\$ 515.36	\$ 13,399.36	
40992	NS 4" BEND	5	EA	\$ 2,766.65	\$ 13,833.25	
41982	NS 4" OFFSET	6	EA	\$ 4,705.65	\$ 28,233.90	
44301	NS FURNISH and INSTALL 24" LINSTOP	2	EA	\$ 73,658.52	\$ 147,317.04	
38900	NS SALTmarsh CORDGRASS, 2" PLUG	20320	EA	\$ 1.95	\$ 39,624.00	
40992	3" BEND	5	EA	\$ 2,169.93	\$ 10,849.65	
42080	8" DI SAN PIPE	365	LF	\$ 93.51	\$ 34,131.15	
40006	2" WATER SERVICE LINE	198	LF	\$ 54.25	\$ 10,741.50	
	Misc				\$ 330,095.57	
	Total				\$ 9,171,862.30	

Submittals and RFI Status

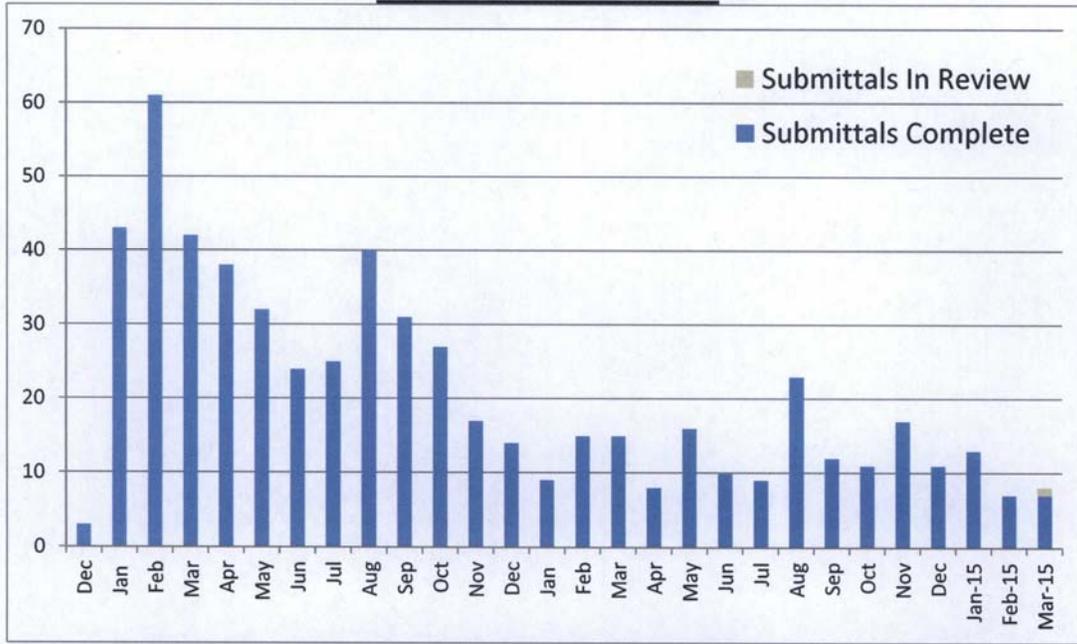

Total Number of Submittals = 581 ; Number of Submittals in review = 1 ;

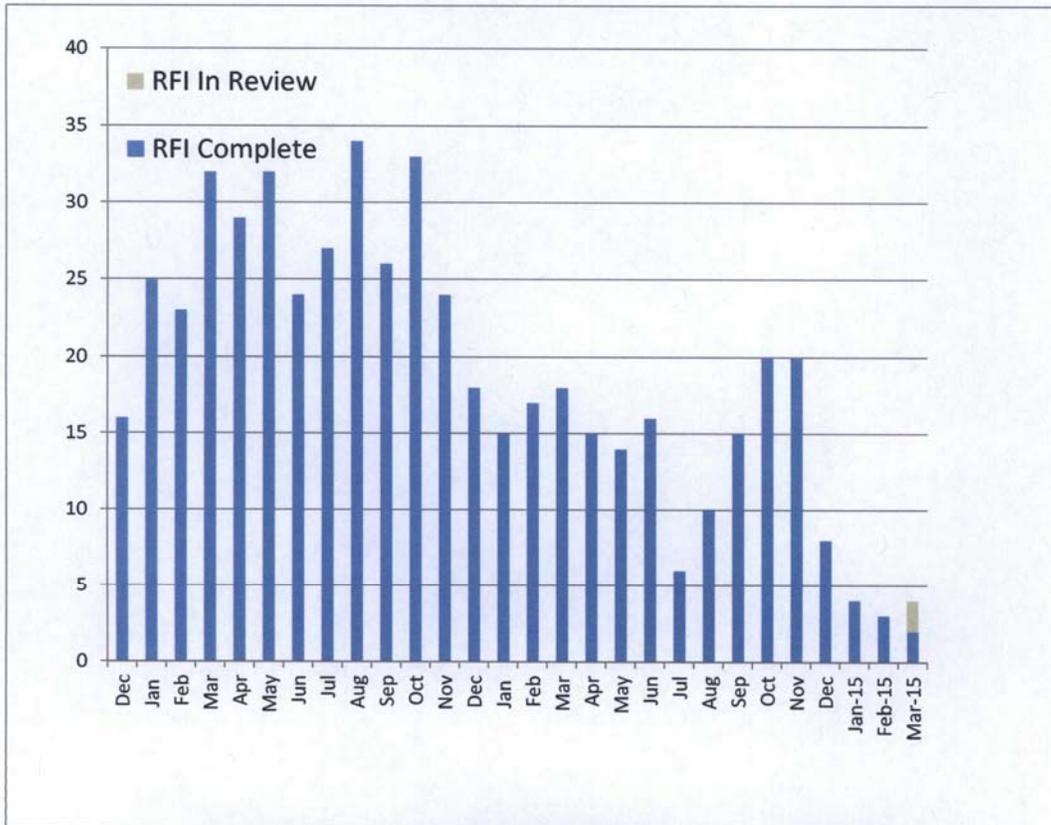

Total Number of RFI = 528 ; Number of RFI in review =2;

SCHEDULE

- The contractor submitted CPM schedule Update 21 with a data date of 3/25/2015. Update 21 has the projected completion on March 22, 2017 which meets the contract completion requirement of April 1, 2017. The following chart summarized the current milestones in DBC's schedule and a comparison of projected Early Finish/Late Finish dates with the February 2015 CPM schedule update.

Milestones

Activity ID	Activity Name	Status	February 2015 Update 20		March 2015 Update 21		Actual Finish
			Early Finish	Late Finish	Early Finish	Late Finish	
1MS1010	Access Road C Complete	Not Completed	6/18/2015	3/31/2017	7/14/2015	3/31/2017	
1MS1030	Great Bridge Blvd Through Ramps complete	Not Completed	6/15/2016	3/31/2017	5/31/2016	3/31/2017	
1MS1040	B615 Complete	Not Completed	2/9/2016	8/31/2016	3/4/2016	8/31/2016	
1MS1045	B614 Complete	Not Completed	2/9/2016	8/31/2016	3/4/2016	8/31/2016	
1MS1110	Ramp N Complete	Not Completed	2/27/2015	9/17/2015	3/27/2015	9/17/2015	
2MS1170	B-608 Complete	Not Completed	2/1/2017	2/9/2017	2/1/2017	2/9/2017	
2MS1190	Ramp F & Bainbridge Blvd. Complete	Not Completed	8/8/2016	2/9/2017	8/29/2016	2/9/2017	
2MS1210	ORT Final Acceptance	Not Completed	3/5/2017	3/31/2017	3/5/2017	3/31/2017	
361EW1200	Station 361 to B614/B615 Complete SB	Not Completed	8/8/2016	2/9/2017	8/29/2016	2/9/2017	
361EW1280	B614/B615 Through Ramps Complete	Not Completed	6/15/2016	12/8/2016	5/31/2016	12/8/2016	
361EW1480	Station 361 to B614/B615 Complete NB	Not Completed	2/9/2016	8/31/2016	3/4/2016	8/31/2016	
3MS1011	Ramps C & D Available for B-609 traffic	Not Completed	11/23/2015	10/7/2016	12/7/2015	10/7/2016	
3MS1020	Phase 3 Complete/ Cedar Mainline	Not Completed	11/23/2015	2/13/2017	12/7/2015	2/13/2017	
3MS1030	Cedar Road/Moses Grandy Complete	Not Completed	6/19/2015	3/31/2017	7/22/2015	3/31/2017	
612-M9000	B612 Complete	Not Completed	10/19/2015	2/9/2017	11/19/2015	2/9/2017	
613-M9000	B613 Complete	Not Completed	11/19/2015	10/5/2016	12/7/2015	10/5/2016	
GBMS1050	Great Bridge Blvd Phase 1 Complete	Not Completed	5/15/2015	3/31/2017	5/27/2015	3/31/2017	
MS0020	Contract Completion	Not Completed	3/22/2017	3/31/2017	3/22/2017	3/31/2017	
MS1020	Early Completion	Not Completed	9/22/2016	9/22/2016	9/22/2016	9/22/2016	
RKEW4150	Ramp K Complete	Not Completed	4/18/2016	3/31/2017	5/5/2016	3/31/2017	
RLEW1080	Place Traffic on completed Ramps R & L	Not Completed	8/5/2016	2/13/2017	7/26/2016	2/13/2017	
ROUT1090	Ramp O Complete	Not Completed	4/18/2016	3/31/2017	5/5/2016	3/31/2017	
AHEW1080	Access Road H Complete	Completed					7/26/2013
609-D1010	Clearing and Access Complete	Completed					3/22/2013
RKUT4110	Ramp K Utilities Complete	Completed					6/10/2013
RNEW1000	Ramp N Ground Improvements (Tied to RKEW4050)	Completed					1/10/2014
2MS1100	Shift Traffic To Detour A	Completed					10/6/2013
3MS1000	Traffic to Temp Ramp A & B	Completed					1/25/2014
1MS1020	Bridge B-616 Complete	Completed					9/29/2014
2MS1110	B-609 Complete	Completed					12/15/2014
2MS1120	B-610 Complete	Completed					12/15/2014
2MS1130	B-611 Complete	Completed					12/15/2014
2MS1140	Shift Traffic to B-609	Completed					12/15/2014
2MS1150	Ramp H Complete	Completed					12/15/2014
2MS1160	Ramp G Complete	Completed					12/15/2014
334EW1170	Ramp G, to Box Culvert Complete	Completed					12/15/2014
RLEW1230	Ramp L Under K Complete	Completed					12/15/2014
361EW1650	609 Abutment B through Ramp H Complete	Completed					12/15/2014
1MS1120	Ramps P & J Complete	Completed					12/2/2014
1MS1130	Ramp I Complete	Completed					12/15/2014
1MS1140	Ramp M Complete	Completed					12/13/2014
1MS1150	Shift Traffic to Phase 2 (Ramps I, L, M, P & under K Complete)	Completed					12/15/2014

Reviewed by: Mike Prezioso, PE, CCM, MBP

cc: Kevin Lundgren, PE, City of Chesapeake
Leon Malczewski, CCM, MBP

Attachment: Progress Photos




03/11/2015 Construction of B612 & B613 Pier 2 (Cedar Rd.)



03/31/2015 Construction of B612 & B613 Pier 2 (Cedar Rd.)



03/11/2015 B608 Deck Construction

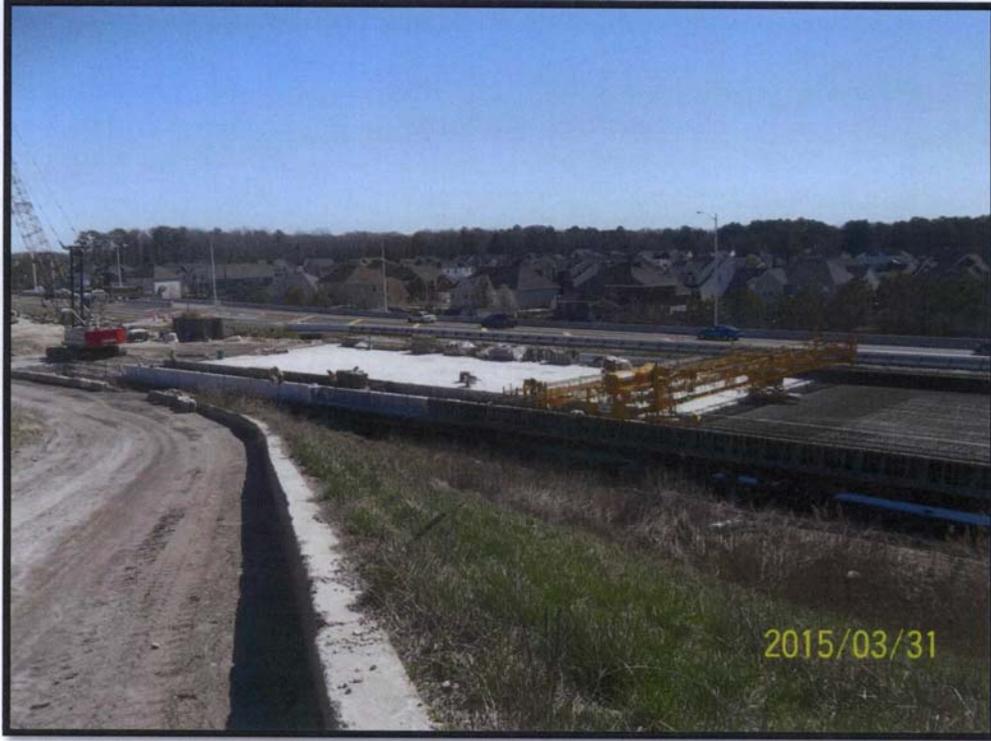

03/31/2015 B608 Deck Construction



03/11/2015 B608- Preparation for deck pour



03/31/2015 B608- Preparation for deck pour



3/11/2015 B609 Bridge/Access C facing North



03/31/2015 B609 Bridge/Access C facing North



03/11/2015 Construction of Relocated Bainbridge Blvd under Dominion Lakes Dr.



03/31/2015 Construction of Relocated Bainbridge Blvd under Dominion Lakes Dr.



03/11/2015 Construction of B612/B613 Abutment A



03/31/2015 Construction of B612/B613 Abutment A
