

Dominion Boulevard Improvements

AC # 01-6004-05

UPC: 56187

**VDOT Project No: (FO) 6017-131-109, PE-101, RW-201,
C-501, B608, B609, B610, B611, B614, B615, B616, D608,
&**

C-502, B612, B613

FHWA No.: HPP-0017-5(023)




Status Report as of November 30, 2014

TABLE OF CONTENTS

DESCRIPTION	PAGE NUMBER
1. PROJECT STATUS – Schedule and Budget	3
2. SIGNIFICANT ACCOMPLISHMENTS (11/01/14 to 11/30/14)	6
3. KEY OPERATIONS UNDERWAY	8
4. ANTICIPATED WORK (12/01/14 to 12/31/14)	10
5. CHANGE ORDERS AND QUANTITY OVERRUNS	11
6. RFI AND SUBMITTAL STATUS	14
7. SCHEDULE MILESTONES	15
ATTACHMENT: Progress Photographs	


PROJECT STATUS (Schedule and Budget)

Schedule		Budget	
Contract Type	Fixed Date	Original Contract Value	\$ 188,070,320
Fixed Contract Completion Date	04/01/2017	Exposure (Pending Change Orders)	\$ 1,447,613
Contract Duration (Days)	1,546	Expenditures (Approved Change Orders)	\$ 5,940,120
Time Extension (Days)	0	Exposure (Projected Quantity Overruns)	\$ 1,543,083
Current Contract Duration (Days)	1,546	Expenditures (Actual Quantity Overruns)	\$ 8,416,568
		11/26/13 Council Resolution-Scope Mod	\$ 3,000,000
Notice to Proceed	01/07/2013	Current Estimated Contract Value	\$ 208,417,704
First Day of Work	01/07/2013	Amount Paid Prior Periods	\$ 119,211,869
Contract Days Elapsed	693	Amount Paid this Period	\$ 4,495,743
Contract Days Remaining	853	Cumulative Amount Paid	\$ 123,707,612
Estimated Completion Date	04/01/2017	Value Stock Piled Materials	\$ 10,967,744
		Total Contract Cost to Date	\$ 134,675,356
% Contract Work Complete	51%		
% Contract Days Elapsed	45%	% Current Estimated Contract Value Paid (Not Including Stored Materials)	59%
% Contract Time Remaining	55%	% Current Estimated Contract Value Remaining	41%

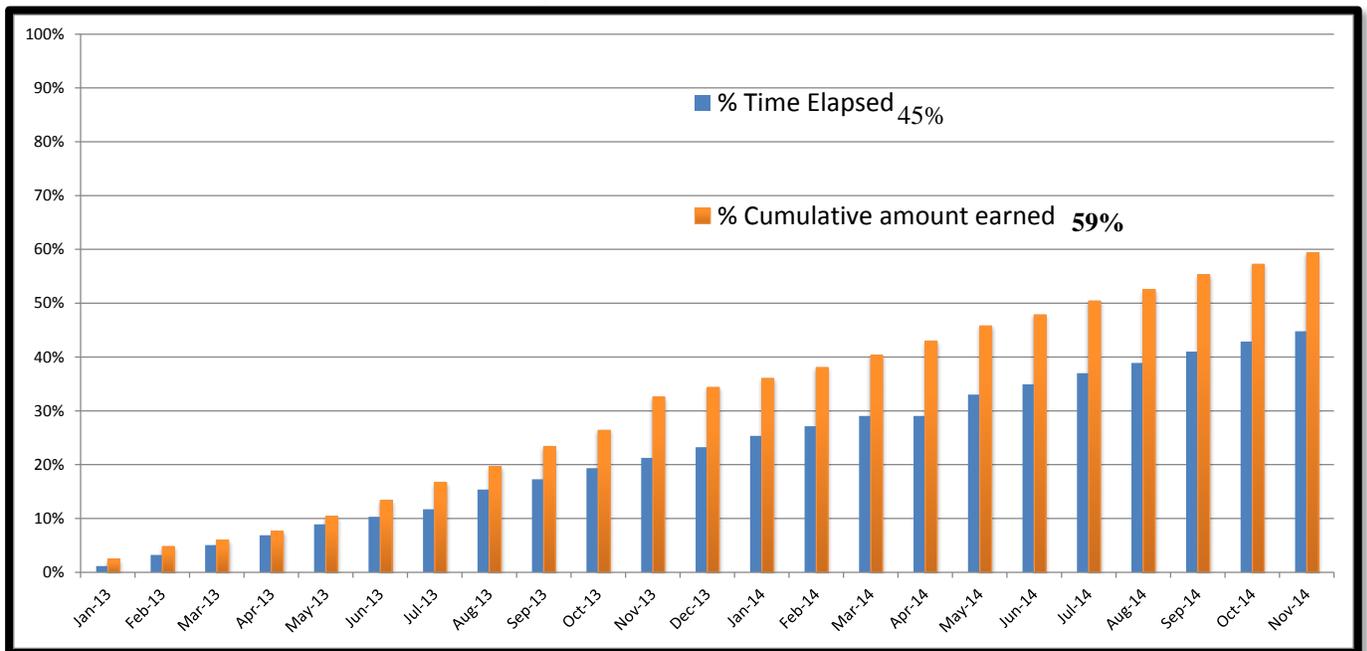

Cumulative amount paid vs Time Elapsed (NTP to November 30, 2014)


SCHEDULE
Actual Percent Work Completed vs. Planned Percent Completed (All Activities)

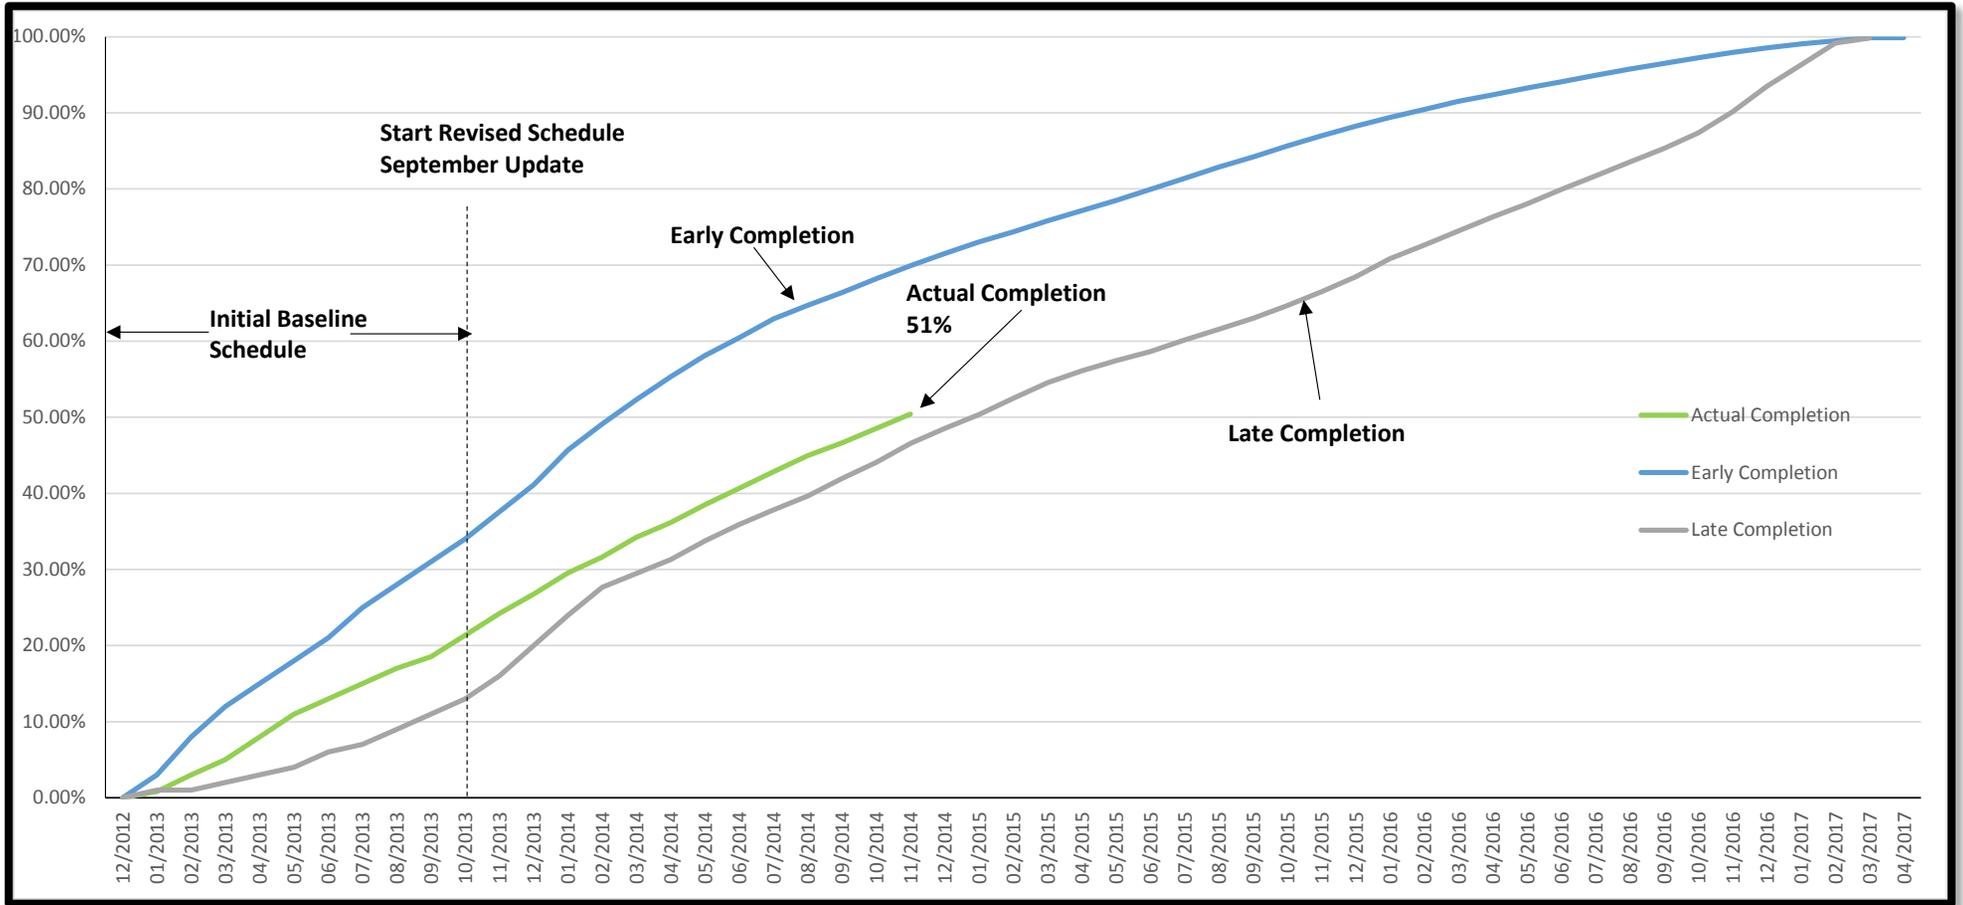

As of November 30, 2014


BUDGET

Actual Contract Cost to Date vs. Planned Contract Cost to Date

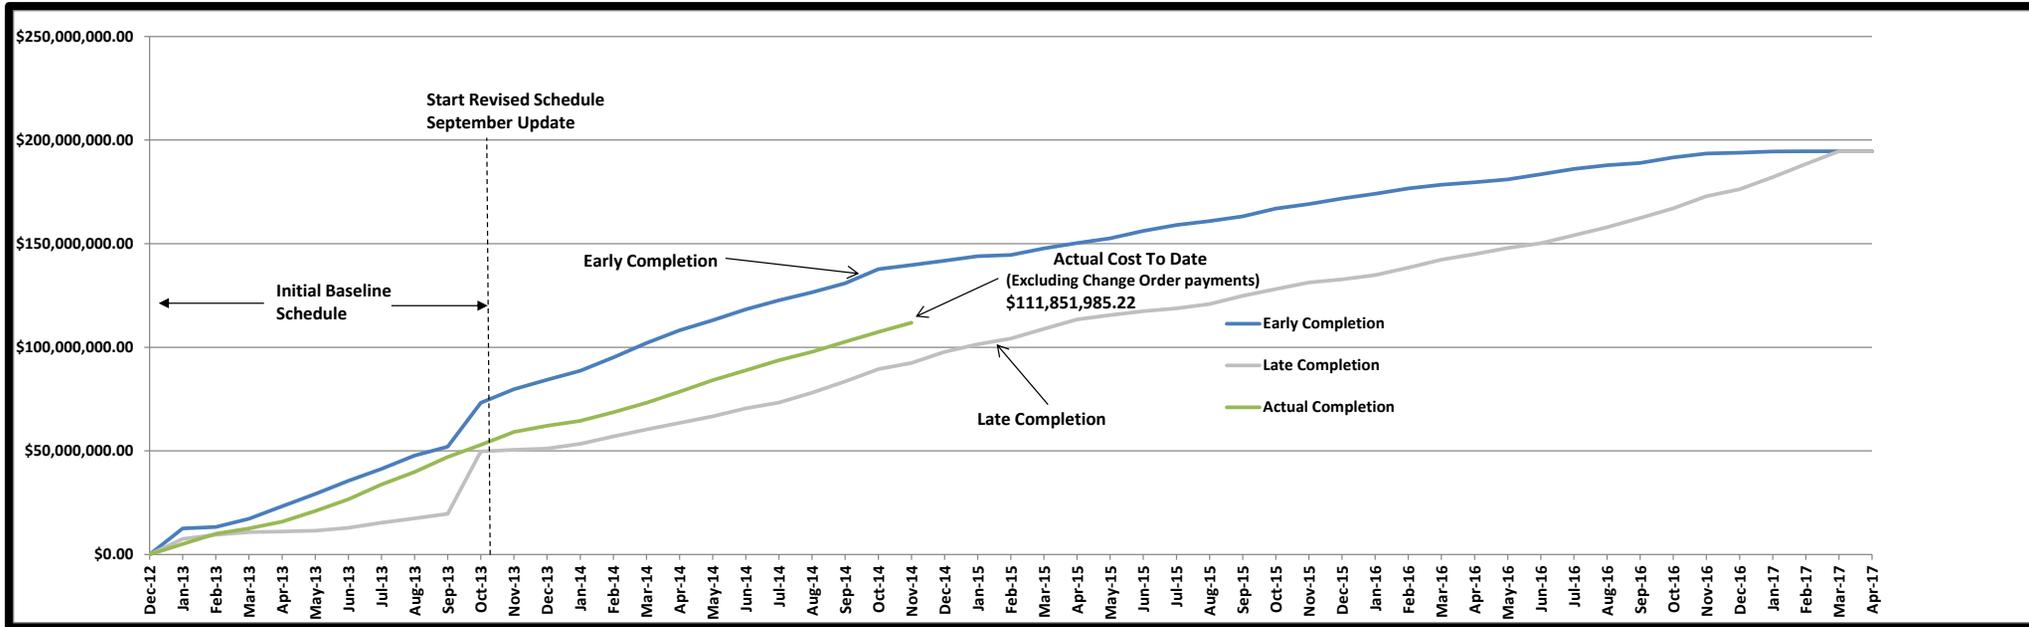

As of November 30, 2014

SIGNIFICANT ACCOMPLISHMENTS THIS MONTH (Nov. 1–Nov. 30, 2014)

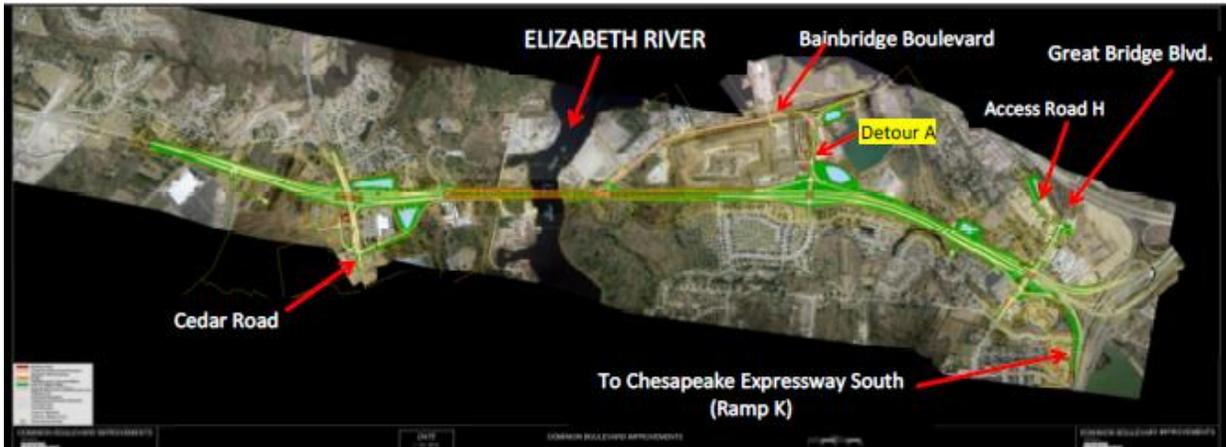

Bridge Descriptions	
<u>B608-</u> Dominion Blvd SB over Elizabeth River	<u>B612-</u> Dominion Blvd SB over Cedar Rd/Moses Grandy Trail
<u>B609-</u> Dominion Blvd NB over Elizabeth River	<u>B613-</u> Dominion Blvd NB over Cedar Rd/Moses Grandy
<u>B610-</u> Dominion Blvd SB over relocated Bainbridge Blvd	<u>B614-</u> Dominion Blvd SB over Great Bridge Blvd
<u>B611-</u> Dominion Blvd NB over Dominion Lakes Blvd/Relocated Bainbridge Blvd.	<u>B615-</u> Dominion Blvd NB over Great Bridge Blvd
	<u>B616-</u> Dom. Blvd./Rte. 168 SB Ramp over Great Bridge Blvd. to I-64 Ramp

Prime Contractor

DBC Joint Venture: (McLean Contracting Co, RR Dawson Bridge Co, Bryant Contracting Inc. and EV Williams Inc.)

Bridge Construction:

B609 (Dominion Blvd NB over Elizabeth River) – *Approximately 98% Complete:*

- Completed bridge deck concrete placement north and south of the river (Completed 42 of 42 spans)
- Completed final preparations for the navigation span deck overlay
- Continued installing bridge railing and parapet
- Completed B608/B609 shared fender system for the current phase (completed 45 of 96 steel HP piles)
- Completed placing concrete for bridge approach slab
- (See Attached Progress Photos)

B608 (Dominion Blvd SB over Elizabeth River) – *Approximately 27% Complete:*

- On-hold pending opening of B609

B616 (Dom. Blvd./Rte. 168 SB Ramp over Great Bridge Blvd. to I-64 Ramp) *100% Complete:*

- Substantially completed Bridge B616 on 9/29/2014

B610 and B611 (Dominion Blvd SB and NB over relocated Bainbridge Blvd) –Approximately 95% Complete:

- Placed concrete for parapets and final bridge tie-ins
- Note: Only B611 is needed for the pending opening of the first phase

B612 and B613 (Dominion Blvd SB and NB over Cedar Rd/Moses Grandy) - Approximately 36% Complete:


- Continued placing concrete for piers and pier cap
- Minimal work pending completion of pre-settlement of abutment embankments

Roadway Construction (DBC, Inc):

- Continued installation of storm drainage system at various locations
- Continued monitoring advanced settlement from embankment surcharges, completed at several locations.
- Continued construction of ramps at north end of project
- Continued placement of Cement Treated Aggregate (CTA) and asphalt for Dominion Blvd. mainline and ramps for opening the first bridge crossing over the Elizabeth River (B611)

Major Subcontractors

- **Bissette Construction Corp**
 - Continued installation of storm drain systems south of Elizabeth River at various locations
- **Virginia Sign and Lighting**
 - Continued installing conduit at various MSE Walls
 - Continued installing lighting conduits at Dominion Lakes
 - Continued installing light poles and lighting controls at various locations
- **Virginia Paving Co**
 - Continued placing asphalt at various location in preparation for opening the first phase of the project
 - Continued placing asphalt in preparation of opening the new southbound ramps to Dominion Blvd. from I464
 - Continued placing asphalt for the ramps from Dominion Boulevard northbound to the Chesapeake Expressway
- **Reliance Concrete Contractors**
 - Continued placing concrete for leveling course and moment slab at MSE Walls 1 & 8
 - Continued placing concrete for curb and gutter at various locations including Great Bridge Blvd. and Access Road C
 - Placed Slope Protection at Ramps J & L
- **Lasting Coastline Inc**
 - Continued setting concrete barrier on various MSE Walls

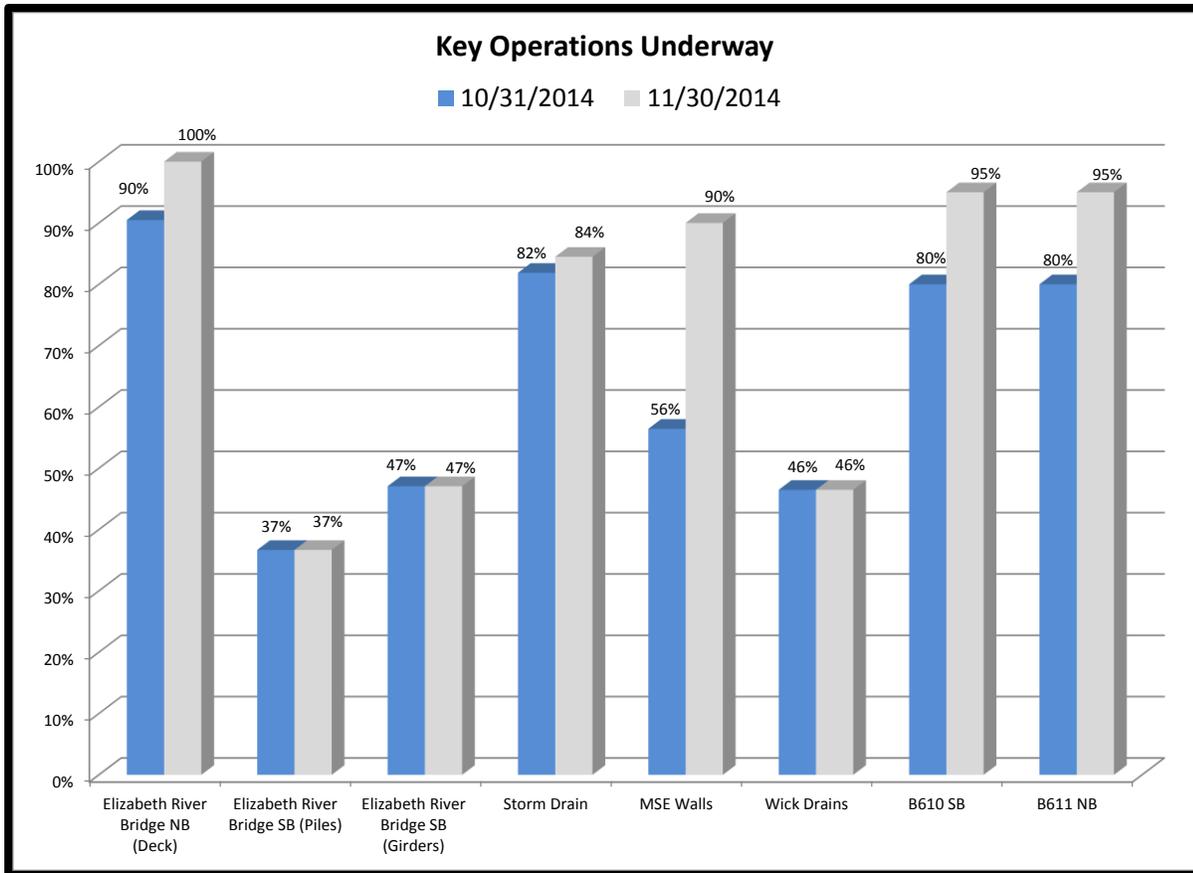


Project Key Operation Status as of 11/30/2014

Key Operations Completed	Month Completed
Elizabeth River Bridge NB (Bent Caps)	Aug-13
Elizabeth River Bridge NB (Piles)	Sep-13
Open Detour A	Oct-13
Elizabeth River Bridge NB (River Footings)	Nov-13
Opened relocated Dom Blvd. at Cedar Road	Jan-14
Partially opened Access A and Access AA	Mar-14
Opened Blake Street	Apr-14
Completed Setting Navigation Span Beams	May-14
Opened permanent intersection for Access A/AA at Cedar Rd.	Jun-14
Completed Stage 1 Post-Tensioning for B609 spliced Girders	Jul-14
Completed Dominion Lakes Blvd. entrance	Aug-14
Completed Driving Piles at B610 and B611	Aug-14
Completed Soil Nail Wall construction	Sep-14
Completed B609 Spliced Girder Post Tensioning	Oct-14
Completed Bridge decks for B609	Nov-14

MAINTENANCE OF TRAFFIC

Lane Closures

- Various temporary lane closures throughout project including night-time closures to minimize impacts to motorists
- Detour A is in place to divert Dominion Blvd traffic and enable start of B608 construction

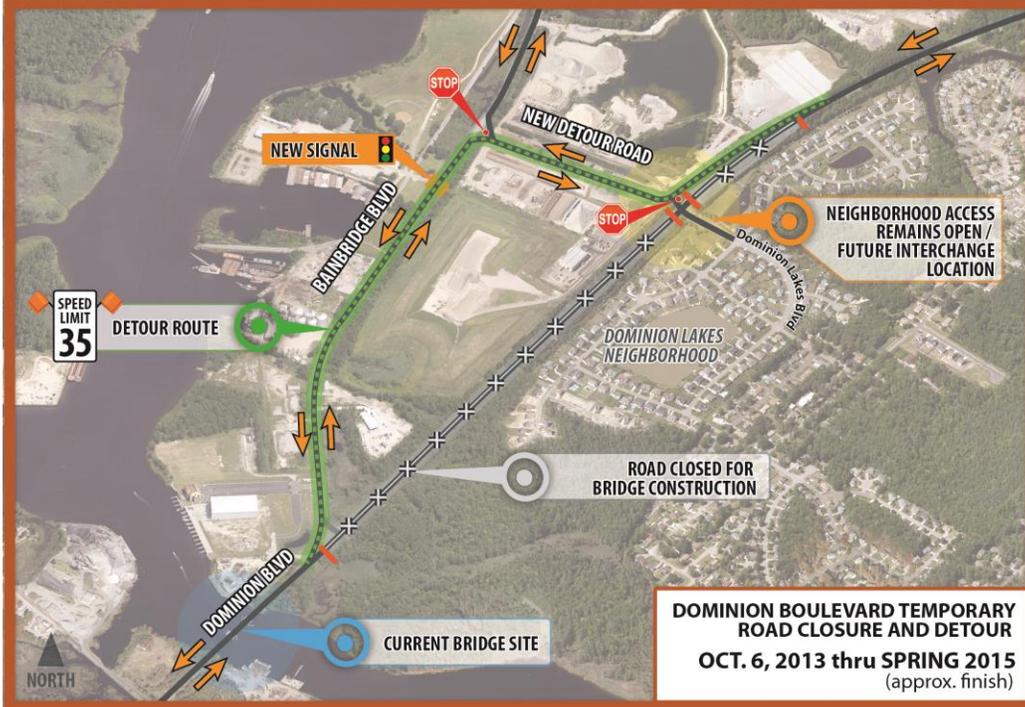

Detour A (Relocated Bainbridge) completed:
(Arrows show temp. traffic pattern for Dominion Blvd.)

- **Ramp P (Rte. 168 N Exit 15B to Dominion Blvd S):** Reopened to traffic 12/1/2014 along with completion of the new southbound ramps from I464 to Dominion Blvd.



Detour Route for Ramp P Closure

- Traffic on Dominion Blvd. remains shifted slightly to a temporary roadway at Moses Grandy to enable construction of B612 and B613 to begin.

ANTICIPATED WORK PLANNED FOR NEXT MONTH (11/01/14 – 11/30/14)

DBC Joint Venture

- B609 (Dominion Blvd. NB Bridge over Elizabeth River)
 - Place concrete for the navigation span overlay
 - Complete concrete placements for parapets and installation of railing
- B608 (Dominion Blvd. SB Bridge over Elizabeth River)
 - On hold pending completion of B609 priorities
 - Begin installation of test piles for river piers
- B616 (Dom. Blvd./Rte. 168 SB Ramp over Great Bridge Blvd. to I-64 Ramp)
 - Completed
- B610 and B611 (Dominion Blvd SB and NB over relocated Bainbridge Blvd)
 - Complete parapets and final tie-ins for B611 to switch traffic with the opening of B609 over the Elizabeth River
- B612 and B613 (Dominion Blvd SB and NB over Cedar Rd/ Moses Grandy)
 - Continue concrete placement for pier footings, columns and caps
- Continue installation of storm drainage systems at various locations
- Continue construction of new Dominion Blvd. including MSE walls for ramps at various locations. Limited work pending the traffic switch for the first phase
- Continue placing cement treated aggregate and preparations for asphalt on Dominion Blvd main line

Roche Brothers

- Continue construction of MSE Walls after switching traffic for the first phase

Reliance Concrete Contractors Inc.

- Continued placing curb at various locations

Virginia Sign and Lighting

- Continue installing temporary and permanent signals at Great Bridge Blvd.
- Continue installing lighting system on B609 and at Dominion Lakes

Virginia Paving

- Continue placing asphalt for permanent ramps and roadway at various locations.



Change Orders

Dominion Boulevard Improvements - Exposure Summary as of November 30, 2014			
12/08/2014 Updated			
Requested Change Orders			
Change Order Number	Scope	Exposure from Change Orders (\$)	Expenditures from Change Orders (\$)
01	Add Flaggers & Portable Changeable Message Signs		\$91,071.25
02	Replace Porous fill with strip drains at MSE Walls		(\$1,444,802.94)
03	Raise B608 & B609 Bridge Footings		(\$810,117.50)
04	Add'l electric service per plan Rev. 1/18/2013		\$139,651.02
05	Add #57 stone to the contract		\$851,600.00
06	Add Trainees to the contract		\$45,000.00
07	2" HDPE Conduit - Bored		\$25,747.68
08	8" Sanitary Force Main Under Wetlands		\$22,601.25
09	B609 Pier 14 Pile Modif.		\$831,940.75
10	Temp. Signal at Bainbridge and Sta. 55+50		\$73,977.55
11	Type D Removable Pavement Markings for Concrete		\$47,400.00
12	Removal of Concrete Barriers (\$12.50/LF)		\$6,000.00
13	Ramp K/MSE Wall 22 Wick Drains		\$305,633.61
14	Demolition/Removal of Existing Sound Wall		\$72,643.23
15	Disposal of Unsuitable Material (base on 140,000 cy)		\$6,025,600.00
16	MSE Walls at Bridge Abutments B610-B615		(\$239,207.30)
17	Delete Aesthetic Treatment		(\$1,838,302.58)
18	4 inch water meters at Great Bridge & Cedar		\$10,772.06
19	Relocation of the Pressure Sensor Telemetry Cabinet; 8/29/2013 Questions to DBC		\$23,457.35
20	Water Meter Vault at DR-1J50-1		\$11,157.98
21	Anti-Graffiti Paint - 8/26 Rec'd DBC's Revised Scope		\$219,823.36
22	16 inch Waterline Repairs at Bainbridge		\$18,116.70
23	Temp. Street lights at Cedar/Dominion Blvd		16,717.73
24	Soil Nail Wall		\$247,184.50
25	12" x 12" x 8" Junction Boxes		\$36,026.55
26	Installation of Leak Detectors Water/Sewer Casings		\$47,359.48
27	New High Mast Light Assembly		\$60,454.18
28	Grass Cutting		\$152,556.48
29	Missing Pay Items: RW2, RW3, Impact Attenuators		\$361,862.19
30	Replace MC-3B Asphalt Curb with Conc. Curb (VEP 07)		-\$39,402.03
31	Remove Existing Sign Structures		\$6,192.66
32	GPS As-Builts of Utilities		\$84,527.20
33	Plan Revision No. 14 Additional Work		\$476,877.44
34	Soil Nail Walls - Additional Work	\$141,766.40	
35	Replace existing junction boxes	\$15,192.04	
36	Wireless System Coaxial Cable for Traffic Signals	\$22,085.04	
37	MSE Wall Redesign	\$318,630.21	
38	Conflict Manhole at 4" Sanitary Force Main	\$8,095.62	
39	CCW Type D Lighting Control Cabinets	\$128,028.30	
(TBD)	VDOT VMS Sign Removal/Reinstall	\$47,883.33	
(TBD)	Structure 32-10 Add.	\$8,929.89	
(TBD)	Plan Rev. No. 8 8" PVC Sewer	\$16,808.21	
(TBD)	Removal of Underground Water Storage Tanks	\$15,065.49	
(TBD)	Installation of Verizon Vaults and Pedestals	\$64,255.85	
(TBD)	24" x 6" Reducer for Additional Fire Hydrant	\$4,172.63	
(TBD)	Obstruction at 18" Jack and Bore	\$67,865.38	
(TBD)	Connection of Existing Sewer Laterals to New, Relocated Sewer Main	\$18,061.62	
(TBD)	Additional Work Associated with Revision 10	\$6,570.40	
(TBD)	Obstructions between Str. 23N-1 and 23N-2	\$23,114.87	
(TBD)	Additional Restrained Waterline	\$10,793.22	
(TBD)	Plan Revision No 12 Added Wick Drains/Survey	\$35,593.37	
(TBD)	Temporary Drainage at Detour A	\$17,634.06	
(TBD)	Waterline Joint Restraint at Great Bridge Blvd.	\$4,701.38	
(TBD)	VMS Conductor Cable	\$19,502.00	
(TBD)	Remove/Salvage Existing Signal Equipment	\$39,115.32	
(TBD)	Plan Revision No. 13 Additional Work	\$19,456.14	
(TBD)	24" Waterline tie-in delays at Cedar Road	\$8,114.82	
(TBD)	B609 Pier No. 3-8 Rebar Changes to Caps	\$21,753.35	
(TBD)	Plan Revision No. 15 Additional Work	\$29,528.83	
(TBD)	VPDES Permit Re-application and Maintenance Fee	\$16,054.35	
(TBD)	Optional Tolling Interoperability Functionality	\$310,626.13	
(TBD)	Remove Existing Sign Structures D704 & D14	\$8,214.60	
NA	RESCINDED: Sewer Force Main Offset Blake/GBB		\$0.00
NA	RESCINDED: Utilities at 18" HRSD (Sta. 22+50 to Sta. 23+00)		\$0.00
NA	RESCINDED: Installation of F-Shaped Conc. Barrier		\$0.00
NA	RESCINDED: Per RFI 191 - Storm Drain		\$0.00
NA	RESCINDED: Relocate HRSD Leak Detector Conflict		\$0.00
NA	RESCINDED: Storm Drain Adjustments		\$0.00
	TOTAL	\$1,447,612.85	\$5,940,119.85



Unit Price Item Quantities – Projected and Actual Overruns

Unit Price Item Quantity Overruns (Projected Quantity Overruns)					
Item Number	Description	Projected Quantity Overrun	Units	Unit Price	Projected Cost Overrun
111	CLEARING AND GRUBBING	28.16	AC	\$ 7,700.00	\$ 216,832.00
120	REGULAR EXCAVATION	37712	CY	\$ 29.00	\$ 1,093,648.00
212	MINOR STRUCTURE EXCAVATION BOX CULVERT	1280	CY	\$ 35.00	\$ 44,800.00
505	BEDDING MATERIAL AGGR. NO. 25 OR 26	2700	TON	\$ 78.50	\$ 211,950.00
27500	GEOTEXTILE FABRIC	24910	SY	\$ 6.70	\$ 166,897.00
525	CONCRETE CLASS A3 MISC.	59	CY	\$ 2,913.26	\$ 171,882.34
2192	30" X 19" ELLIPTICAL CONC. PIPE	341	LF	\$ 150.00	\$ 51,150.00
27550	STORMWATER MANAGEMENT DRAINAGE STRUCTURE SWM-1	22	LF	\$ 6,232.87	\$ 137,123.14
9148	EROSION CONTROL STONE (CLASS A1), EC-1	978	SY	\$ 111.98	\$ 109,516.44
9150	EROSION CONTROL STONE (CLASS I), EC-1	3610	SY	\$ 147.48	\$ 532,402.80
85003	UNDERCUT EXC @ TWICE REG EXC	34976.43	CY	\$ 50.00	\$ 1,748,821.50
10636	ASPHALT CONCRETE TY. SM-9.5D	1750	TON	\$ 75.00	\$ 131,250.00
13487	MEDIAN BARRIER MB-8A TYPE III	348	LF	\$ 162.83	\$ 56,664.84
22643	FENCE FE-CL	3800	LF	\$ 12.19	\$ 46,322.00
27321	PROTECTIVE COVERING EC-2	84383	SY	\$ 1.35	\$ 113,917.05
13570	NS RETAINING WALL SOIL NAIL	626.00	SF	\$ 200.04	\$ 125,225.04
13570	NS RETAINING WALL MSE	5000	SF	\$ 56.37	\$ 281,850.00
13570	NS RETAINING WALL TEMPORARY	11400	SF	\$ 30.00	\$ 342,000.00
2093	NS PRE-DRILLING OF WICK DRAINS	851250.725	LF	\$ 1.85	\$ 1,574,813.84
515	TEMPORARY SHEET PILING	10000	SF	\$ 25.00	\$ 250,000.00
10065	AGGR. MATL. NO. 1	1000	TON	\$ 35.91	\$ 35,910.00
24283	POLICE PATROL	1200	HR	\$ 42.40	\$ 50,880.00
56052	BORED CONDUIT 4"	31580	LF	\$ 32.90	\$ 1,038,982.00
56053	2" PVC CONDUIT	36330	LF	\$ 2.25	\$ 81,742.50
56055	4" PVC CONDUIT	12393.04	LF	\$ 4.81	\$ 59,610.52
64424	PRESTR. CONCRETE PILES 24"	400.6	LF	\$ 80.00	\$ 32,048.00
64868	DRIVING TEST FOR 24" PRESTR. CONC. PILE	237	LF	\$ 150.00	\$ 35,550.00
64416	PRESTR. CONCRETE PILES 16"	770.77	LF	\$ 65.00	\$ 50,100.05
40081	8" DI WATER MAIN	1220	LF	\$ 47.74	\$ 58,242.80
42080	8" PVC SAN PIPE	269.35	LF	\$ 157.15	\$ 42,328.35
41982	NS 4" OFFSET	6	EA	\$ 4,705.65	\$ 28,233.90
44301	NS FURNISH and INSTALL 24" LINSTOP	2	EA	\$ 73,658.52	\$ 147,317.04
38900	NS SALT MARSH CORDGRASS, 2" PLUG	20320	EA	\$ 1.95	\$ 39,624.00
42080	8" DI SAN PIPE	365	LF	\$ 93.51	\$ 34,131.15
	Miscellaneous				\$ 817,884.67
	Total				\$ 9,959,650.98




Unit Price Item Quantity Overruns (Actual Quantity Overruns)						
Line Item Number	Item Number	Description	Actual Quantity Overrun	Units	Unit Price	Actual Cost Overrun
3	111	CLEARING AND GRUBBING	28.16	AC	\$ 7,700.00	\$ 216,832.00
4	120	REGULAR EXCAVATION	37684.75	CY	\$ 29.00	\$ 1,092,857.75
8	212	MINOR STRUCTURE EXCAVATION BOX CULVERT	1182.83	CY	\$ 35.00	\$ 41,399.05
9	505	BEDDING MATERIAL AGGR. NO. 25 OR 26	2684.6	TON	\$ 78.50	\$ 210,741.10
10	27500	GEOTEXTILE FABRIC	24872.42	SY	\$ 6.70	\$ 166,645.21
11	525	CONCRETE CLASS A3 MISC.	34.01	CY	\$ 2,913.26	\$ 99,079.97
28	2192	30" X 19" ELLIPTICAL CONC. PIPE	341	LF	\$ 150.00	\$ 51,150.00
31	2292	45" X 29" ELLIPTICAL CONC. PIPE	48	LF	\$ 252.39	\$ 12,114.72
106	27550	STORMWATER MANAGEMENT DRAINAGE	13.3	LF	\$ 6,232.87	\$ 82,897.17
124	9148	EROSION CONTROL STONE (CLASS A1), EC-1	772.33	SY	\$ 111.98	\$ 86,485.51
125	9150	EROSION CONTROL STONE (CLASS I), EC-1	3531.42	SY	\$ 147.48	\$ 520,813.82
132	85003	UNDERCUT EXC @ TWICE REG EXC	34908.67	CY	\$ 50.00	\$ 1,745,433.50
142	10417	TACK COAT	1597.19	GAL	\$ 15.90	\$ 25,395.32
170	13487	MEDIAN BARRIER MB-8A TYPE III	348	LF	\$ 162.83	\$ 56,664.84
194	24602	REMOVE EXISTING (FENCE)	6771	LF	\$ 3.18	\$ 21,531.78
196	51910	SAW CUT	8340	LF	\$ 2.07	\$ 17,263.80
210	27321	PROTECTIVE COVERING EC-2	81677.05	SY	\$ 1.35	\$ 110,264.02
219	13570	NS RETAINING WALL SOIL NAIL	626	SF	\$ 200.04	\$ 125,225.04
221	13570	NS RETAINING WALL TEMPORARY	11326.3	SF	\$ 30.00	\$ 339,789.00
224	2093	NS PRE-DRILLING OF WICK DRAINS	622209	LF	\$ 1.85	\$ 1,151,086.65
229	64808	DRIVING TEST FOR PRESTRESSED CONCRETE PILES	464	LF	\$ 55.00	\$ 25,520.00
246	27410	CHECK DAM, ROCK-TYPE I	31	EA	\$ 370.67	\$ 11,490.77
251	27526	TURBIDITY CURTAIN, IMPERVIOUS	1226	LF	\$ 18.02	\$ 22,092.52
254	515	TEMPORARY SHEET PILING	6806.43	SF	\$ 25.00	\$ 170,160.75
255	10065	AGGR. MATL. NO. 1	291.3592	TON	\$ 35.91	\$ 10,462.71
263	24283	POLICE PATROL	354.08	HR	\$ 42.40	\$ 15,012.99
385	56052	BORED CONDUIT 4"	31261	LF	\$ 32.90	\$ 1,028,486.90
386	56053	2" PVC CONDUIT	8704	LF	\$ 2.25	\$ 19,584.00
388	56055	4" PVC CONDUIT	4630	LF	\$ 4.81	\$ 22,270.30
521	536	NS CONCRETE CLASS A5, SPLICED GIRDER DECK, 5 KSI	24	CY	\$ 650.00	\$ 15,600.00
540	64101	DYNAMIC PILE TEST (FRICTION PILES)	4.333	EA	\$ 3,000.00	\$ 12,999.00
541	64416	PRESTR. CONCRETE PILES 16"	338	LF	\$ 65.00	\$ 21,970.00
542	64424	PRESTR. CONCRETE PILES 24"	400.6	LF	\$ 80.00	\$ 32,048.00
550	64868	DRIVING TEST FOR 24" PRESTR. CONC. PILE	237	LF	\$ 150.00	\$ 35,550.00
562	60404	CONCRETE CLASS A4	24.6	CY	\$ 580.00	\$ 14,268.00
580	60404	CONCRETE CLASS A4	25.7	CY	\$ 580.00	\$ 14,906.00
628	64416	PRESTR. CONCRETE PILES 16"	335	LF	\$ 60.00	\$ 20,100.00
646	66921	NS BRIDGE SUB-STRUCTURE PRE-BORING (16" PRESTR)	460	LF	\$ 25.00	\$ 11,500.00
690	61704	CORROSION RESISTANT REINF. STEEL (Plan Quantity)	5690	LB	\$ 1.80	\$ 10,242.00
709	40061	6" DI WATER MAIN	483	LF	\$ 42.31	\$ 20,435.73
710	40081	8" DI WATER MAIN	753.84	LF	\$ 47.74	\$ 35,988.32
712	40121	12" DI WATER MAIN	202	LF	\$ 83.54	\$ 16,875.08
713	40161	16" DI WATER MAIN	147	LF	\$ 86.80	\$ 12,759.60
718	40408	18" BEND	4	EA	\$ 2,820.91	\$ 11,283.64
721	40992	NS 8" BEND	26	EA	\$ 515.36	\$ 13,399.36
723	40992	NS 4" BEND	7	EA	\$ 2,766.65	\$ 19,366.55
759	41982	NS 4" OFFSET	6	EA	\$ 4,705.65	\$ 28,233.90
784	44301	NS FURNISH and INSTALL 24" LINSTOP	2	EA	\$ 73,658.52	\$ 147,317.04
805	38900	NS SALT MARSH CORDGRASS, 2" PLUG	20320	EA	\$ 1.95	\$ 39,624.00
827	40992	3" BEND	5	EA	\$ 2,169.93	\$ 10,849.65
840	42080	8" DI SAN PIPE	365	LF	\$ 93.51	\$ 34,131.15
848	40006	2" WATER SERVICE LINE	198	LF	\$ 54.25	\$ 10,741.50
		Misc				\$ 327,627.78
						\$ 8,416,567.51


Summary Unit Price Item Overruns:

Current Projected Quantity Overruns	\$ 9,959,650.98
Actual Quantity Overruns	\$ 8,416,567.51
Net Projected Quantity Overruns	\$ 1,543,083.47

Submittals and RFI Status

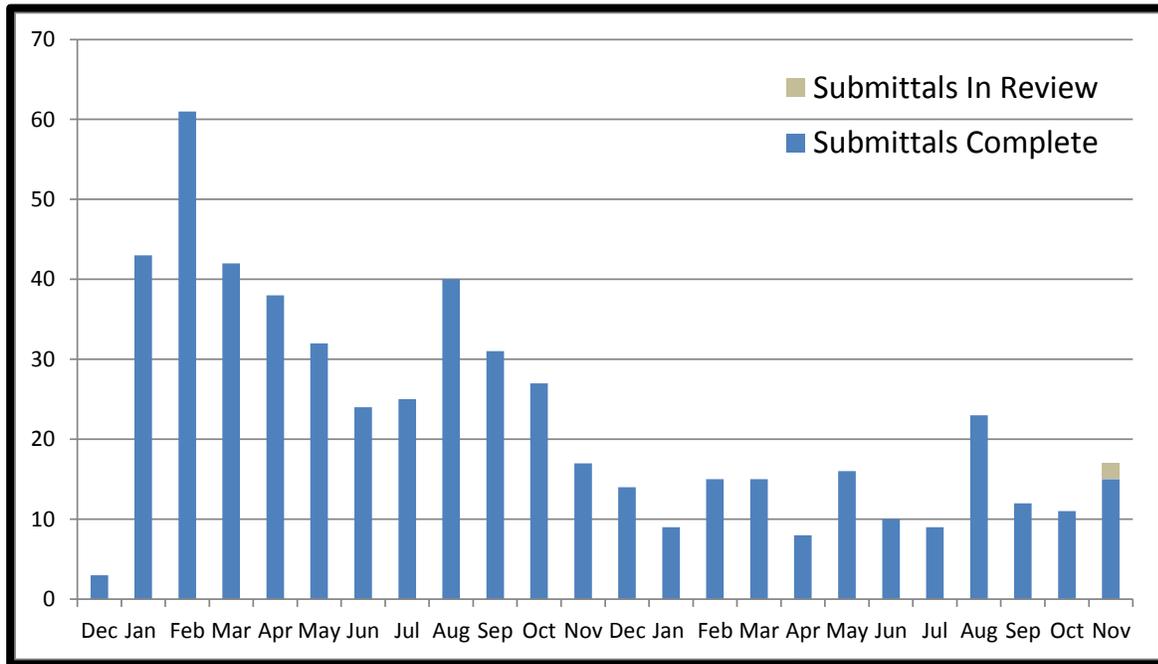

Total Number of Submittals = 542 ; Number of Submittals in review = 2 ;

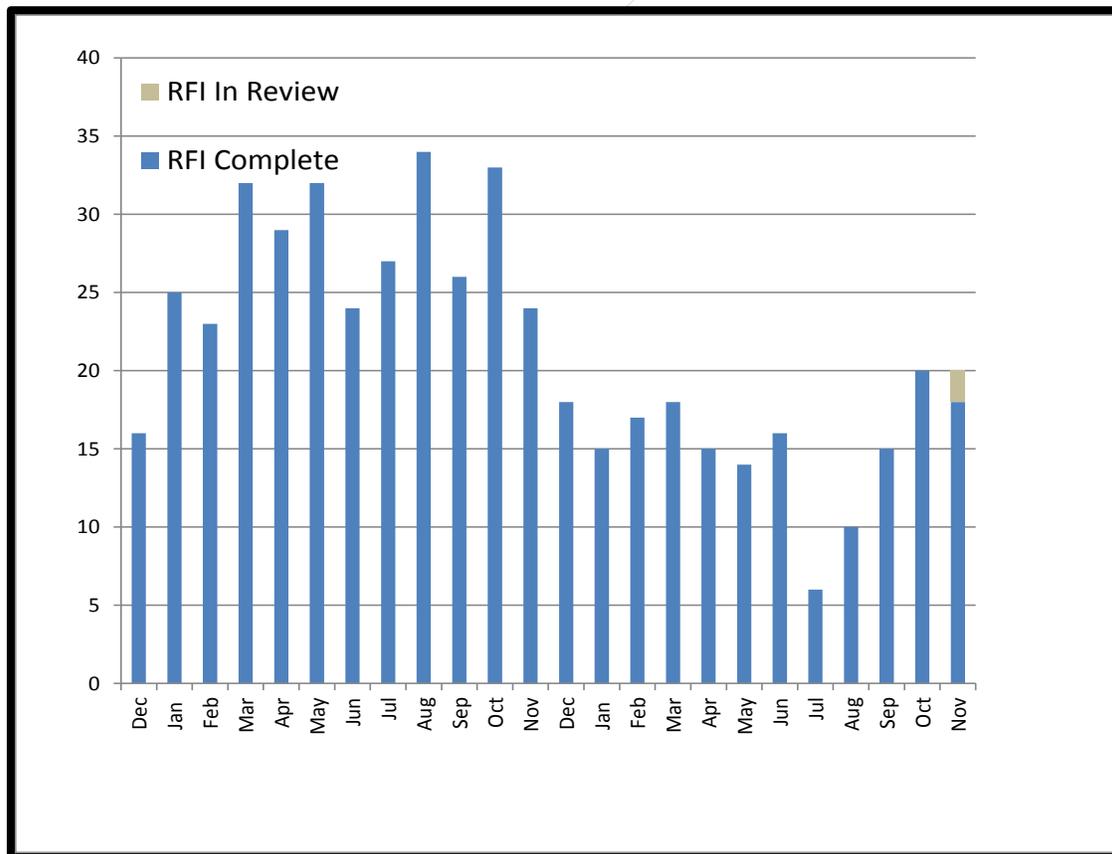

Total Number of RFI = 509 ; Number of RFI in review =2;

SCHEDULE

- The contractor submitted CPM schedule Update 16 with a data date of 10/25/2014. Update 16 has the projected completion on March 31, 2017 which meets the contract completion requirement of April 1, 2017. The following chart summarized the current milestones in DBC's schedule and a comparison of projected Early Finish/Late Finish dates with the August 2014 CPM schedule update

Milestones

Activity ID	Activity Name	Status	September 2014 Update 15		October 2014 Update 16		Actual Finish
			Early Finish	Late Finish	Early Finish	Late Finish	
1MS1010	Access Road C Complete	Not Completed	2/13/2015	2/17/2015	2/5/2015	2/17/2015	
1MS1030	Great Bridge Blvd Through Ramps complete	Not Completed	6/23/2016	3/31/2017	6/17/2016	3/31/2017	
1MS1040	B615 Complete	Not Completed	4/21/2016	3/31/2017	4/15/2016	3/31/2017	
1MS1045	B614 Complete	Not Completed	4/21/2016	3/31/2017	4/15/2016	3/31/2017	
1MS1110	Ramp N Complete	Not Completed	12/11/2014	8/20/2015	1/13/2015	8/20/2015	
1MS1120	Ramps P & J Complete	Not Completed	1/15/2015	8/20/2015	2/3/2015	8/20/2015	
1MS1130	Ramp I Complete	Not Completed	10/31/2014	9/30/2015	12/3/2014	9/30/2015	
1MS1140	Ramp M Complete	Not Completed	10/29/2014	9/30/2015	11/3/2014	9/30/2015	
1MS1150	Shift Traffic to Phase 2 (Ramps I, L, M, P & under K Complete)	Not Completed	3/25/2015	8/20/2015	3/19/2015	8/20/2015	
2MS1110	B-609 Complete	Not Completed	2/17/2015	2/17/2015	2/17/2015	2/17/2015	
2MS1120	B-610 Complete	Not Completed	11/26/2014	3/31/2017	12/1/2014	3/31/2017	
2MS1130	B-611 Complete	Not Completed	11/26/2014	2/17/2015	11/26/2014	2/17/2015	
2MS1140	Shift Traffic to B-609	Not Completed	2/17/2015	2/17/2015	2/17/2015	2/17/2015	
2MS1150	Ramp H Complete	Not Completed	10/29/2014	2/17/2015	12/1/2014	2/17/2015	
2MS1160	Ramp G Complete	Not Completed	1/16/2015	2/17/2015	2/13/2015	2/17/2015	
2MS1170	B-608 Complete	Not Completed	3/29/2017	3/31/2017	3/29/2017	3/31/2017	
2MS1180	Close Ramps G, H, Dominion Lakes & DetourA	Not Completed	2/17/2015	11/21/2016	2/17/2015	11/21/2016	
2MS1190	Ramp F & Bainbridge Blvd. Complete	Not Completed	8/22/2016	3/31/2017	8/15/2016	3/31/2017	
334EW1170	Ramp G, to Box Culvert Complete	Not Completed	10/27/2014	2/17/2015	11/28/2014	2/17/2015	
361EW1200	Station 361 to B614/B615 Complete SB	Not Completed	8/22/2016	3/31/2017	8/15/2016	3/31/2017	
361EW1480	Station 361 to B614/B615 Complete NB	Not Completed	4/21/2016	3/31/2017	4/15/2016	3/31/2017	
361EW1650	609 Abutment B through Ramp H Complete	Not Completed	10/29/2014	2/17/2015	12/1/2014	2/17/2015	
3MS1011	Ramps C & D Available for B-609 traffic	Not Completed	4/13/2015	8/7/2015	4/10/2015	8/7/2015	
3MS1020	Phase 3 Complete	Not Completed	10/18/2016	3/31/2017	10/10/2016	3/31/2017	
3MS1030	Cedar Road/Moses Grandy Complete	Not Completed	10/14/2015	3/31/2017	11/13/2015	3/31/2017	
612-M9000	B612 Complete	Not Completed	10/14/2015	3/30/2017	11/12/2015	3/30/2017	
613-M9000	B613 Complete	Not Completed	8/26/2015	3/30/2017	9/29/2015	3/30/2017	
GBMS1050	Great Bridge Blvd Phase 1 Complete	Not Completed	2/11/2015	8/20/2015	3/19/2015	8/20/2015	
MS0020	Contract Completion	Not Completed	3/29/2017	3/31/2017	3/29/2017	3/31/2017	
MS1020	Early Completion	Not Completed	9/22/2016	9/22/2016	9/22/2016	9/22/2016	
RKEW4150	Ramp K Complete	Not Completed	10/27/2014	8/20/2015	11/6/2014	8/20/2015	
RLEW1080	Place Traffic on completed Ramps R & L	Not Completed	10/18/2016	3/31/2017	10/10/2016	3/31/2017	
RLEW1230	Ramp L Under K Complete	Not Completed	10/16/2014	8/20/2015	11/7/2014	8/20/2015	
ROUT1090	Ramp O Complete	Not Completed	3/25/2015	8/20/2015	2/5/2015	8/20/2015	
AHEW1080	Access Road H Complete	Completed					7/26/2013
609-D1010	Clearing and Access Complete	Completed					3/22/2013
RKUT4110	Ramp K Utilities Complete	Completed					6/10/2013
RNEW1000	Ramp N Ground Improvements (Tied to RKEW4050)	Completed					1/10/2014
2MS1100	Shift Traffic To Detour A	Completed					10/6/2013
3MS1000	Traffic to Temp Ramp A & B	Completed					1/25/2014
1MS1020	Bridge B-616 Complete	Completed					9/29/2014

Reviewed by: Mike Prezioso, PE, CCM, MBP

cc: Kevin Lundgren, PE, City of Chesapeake
Leon Malczewski, CCM, MBP

Attachment: Progress Photos



11/03/2014 Construction of B612 & B613 Pier 2 (Cedar Rd.)



12/05/2014 Construction of B612 & B613 Pier 2 (Cedar Rd.)



11/03/2014 B608 Girder Placement on Bent Caps



12/05/2014 B608 Girder Placement on Bent Caps



12/05/2014 B609 Bridge Deck - Looking South



12/05/2014 B609 Bridge/Access C facing North



11/03/2014 Construction of B612/B613



12/05/2014 Construction of B612/B613



11/03/2014 Construction of B610/B611 over Dominion Lakes Dr.



12/05/2014 Construction of B610/B611 over Dominion Lakes Dr.



11/03/2014 Construction of B612/B613 Abutment A



12/05/2014 Construction of B612/B613 Abutment B
