

Dominion Boulevard Improvements

AC # 01-6004-05

UPC: 56187

**VDOT Project No: (FO) 6017-131-109, PE-101, RW-201,
C-501, B608, B609, B610, B611, B614, B615, B616, D608,
&**

C-502, B612, B613

FHWA No.: HPP-0017-5(023)




Status Report as of August 31, 2014

TABLE OF CONTENTS


DESCRIPTION	PAGE NUMBER
1. PROJECT STATUS – Schedule and Budget	3
2. SIGNIFICANT ACCOMPLISHMENTS (08/01/14 to 08/31/14)	6
3. KEY OPERATIONS UNDERWAY	8
4. ANTICIPATED WORK (09/01/14 to 09/30/14)	10
5. CHANGE ORDERS AND QUANTITY OVERRUNS	12
6. RFI AND SUBMITTAL STATUS	14
7. SCHEDULE MILESTONES	15
ATTACHMENT: Progress Photographs	

PROJECT STATUS (Schedule and Budget)

Schedule		Budget	
Contract Type	Fixed Date	Original Contract Value	\$ 188,070,320
Fixed Contract Completion Date	04/01/2017	Exposure (Pending Change Orders)	\$ 3,190,020
Contract Duration (Days)	1,546	Expenditures (Approved Change Orders)	\$ 4,251,823
Time Extension (Days)	0	Exposure (Projected Quantity Overruns)	\$ 1,726,589
Current Contract Duration (Days)	1,546	Expenditures (Actual Quantity Overruns)	\$ 7,677,064
		11/26/13 Council Resolution-Scope Mod	\$ 3,000,000
Notice to Proceed	01/07/2013	Current Estimated Contract Value	\$ 207,915,816
First Day of Work	01/07/2013	Amount Paid Prior Periods	\$ 105,134,770
Contract Days Elapsed	602	Amount Paid this Period	\$ 4,274,214
Contract Days Remaining	944	Cumulative Amount Paid	\$ 109,408,984
Estimated Completion Date	04/01/2017	Value Stock Piled Materials	\$ 12,119,783
		Total Contract Cost to Date	\$ 121,528,767
% Contract Work Complete	44%		
% Contract Days Elapsed	39%	% Current Estimated Contract Value Paid (Not Including Stored Materials)	53%
% Contract Time Remaining	61%	% Current Estimated Contract Value Remaining	47%

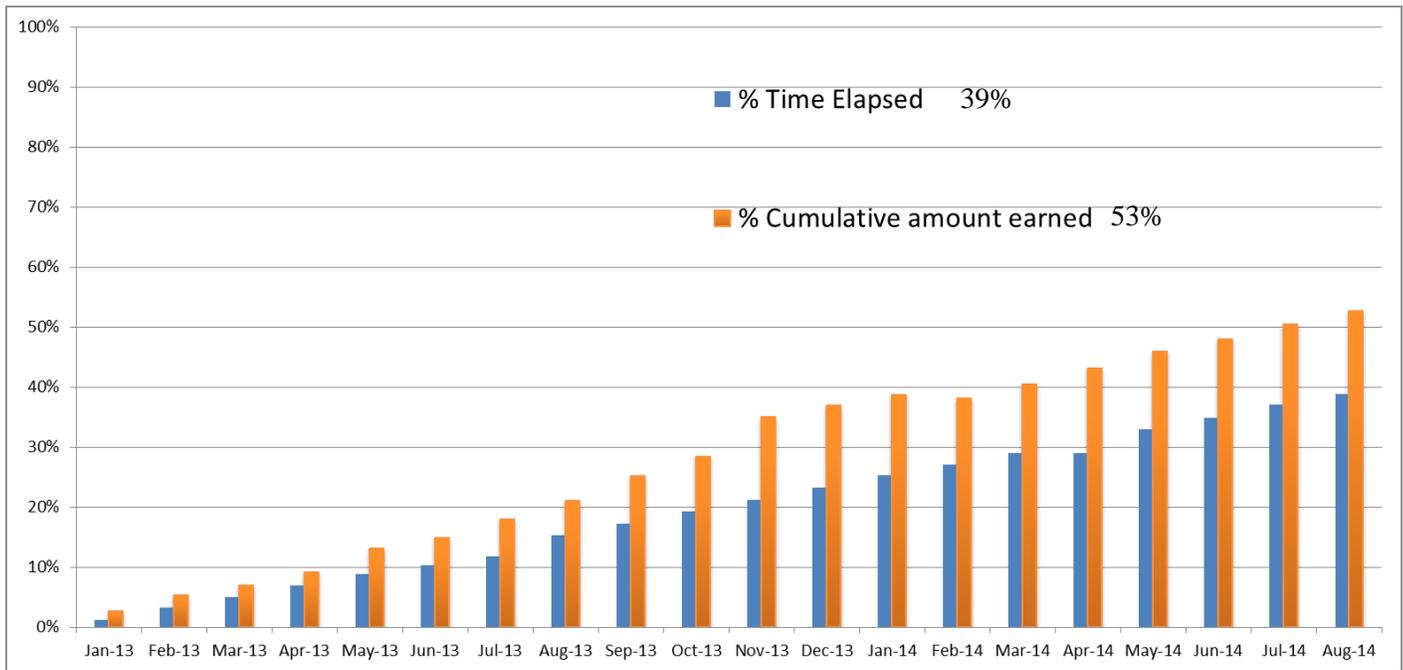


SCHEDULE
Actual Percent Work Completed vs. Planned Percent Completed (All Activities)

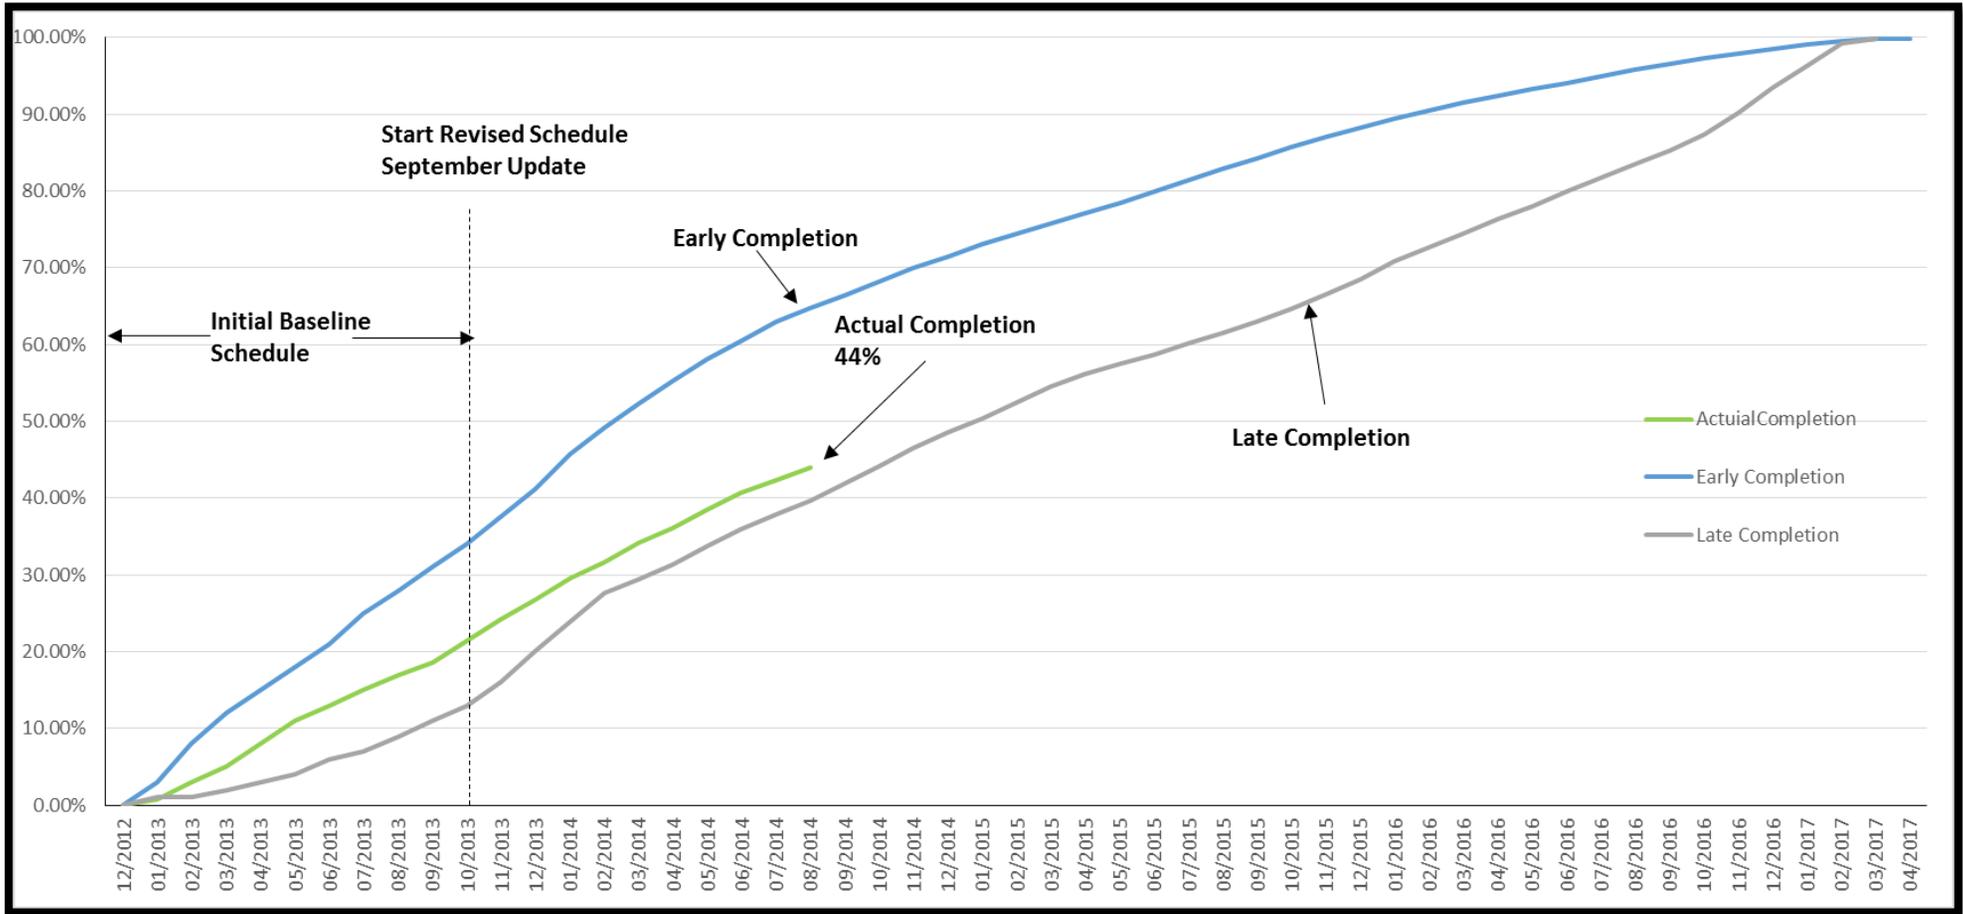


As of August 31, 2014

BUDGET
Actual Contract Cost to Date vs. Planned Contract Cost to Date

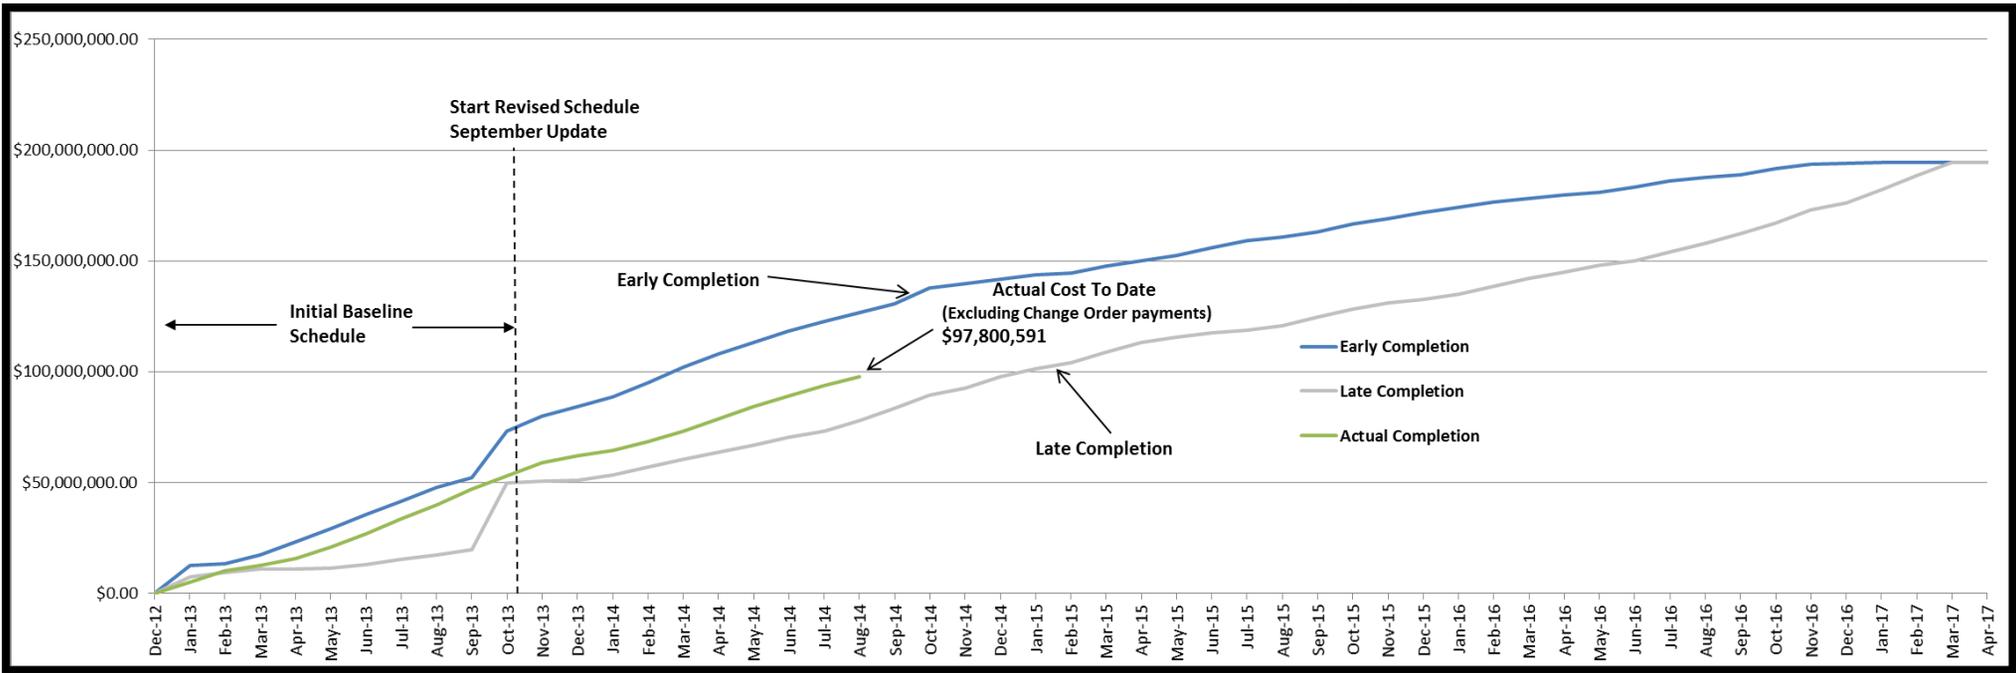

As of August 31, 2014

SIGNIFICANT ACCOMPLISHMENTS THIS MONTH (Aug. 1–Aug. 31, 2014)

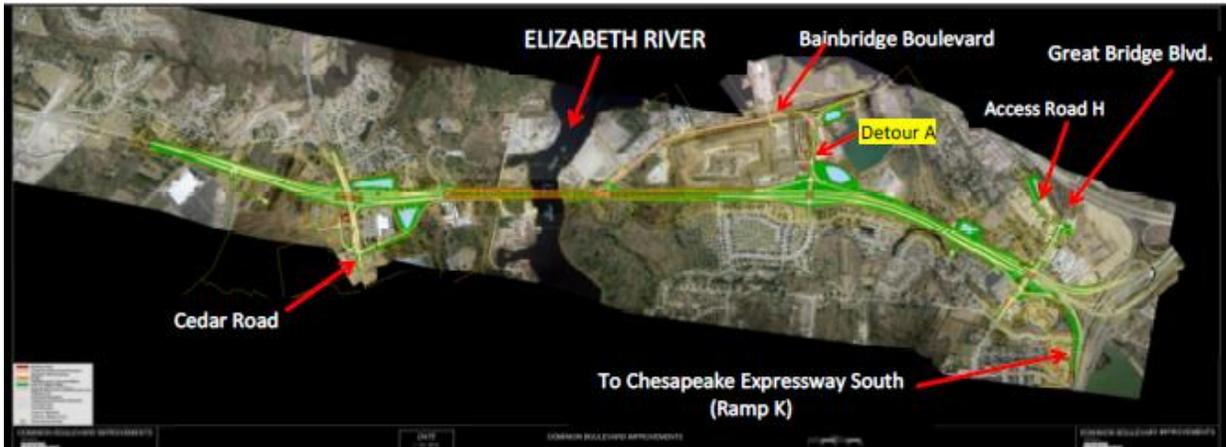

Bridge Descriptions	
B608- Dominion Blvd SB over Elizabeth River	B612- Dominion Blvd SB over Cedar Rd/Moses Grandy Trail
B609- Dominion Blvd NB over Elizabeth River	B613- Dominion Blvd NB over Cedar Rd/Moses Grandy
B610- Dominion Blvd SB over relocated Bainbridge Blvd	B614- Dominion Blvd SB over Great Bridge Blvd
B611- Dominion Blvd NB over Dominion Lakes Blvd/Relocated Bainbridge Blvd.	B615- Dominion Blvd NB over Great Bridge Blvd
	B616- Dom. Blvd./Rte. 168 SB Ramp over Great Bridge Blvd. to I-64 Ramp

Prime Contractor

DBC Joint Venture: (McLean Contracting Co, RR Dawson Bridge Co, Bryant Contracting Inc. and EV Williams Inc.)

Bridge Construction:

B609 (Dominion Blvd NB over Elizabeth River) - *Approximately 85% Complete:*

- Continued bridge deck concrete placement north and south of the river (Completed 33 of 42 spans)
- Continued installing bridge railing and parapet
- Completed concrete placement for the abutment caps
- Continued B608/B609 shared fender system (completed 31 of 96 steel HP piles)
- Continued formwork in preparation of the navigation span deck concrete placement
- (See Attached Progress Photos)

B608 (Dominion Blvd SB over Elizabeth River) – *Approximately 22% Complete:*

- Continued placing concrete for footings, columns and caps
- Continued installing girders on bent caps

**B616 (Dom. Blvd./Rte. 168 SB Ramp over Great Bridge Blvd. to I-64 Ramp) -
Approximately 99% Complete:**

- Began concrete placements for bridge parapets.

**B610 and B611 (Dominion Blvd SB and NB over relocated Bainbridge Blvd) –Approximately
45% Complete**

- Completed concrete placement for B610 integral backwalls
- Completed concrete placement for B611 integral backwalls
- Begin preparations for deck formwork

**B612 and B613 (Dominion Blvd SB and NB over Cedar Rd/Moses Grandy) - Approximately
25% Complete:**

- Continued driving piles for abutments and piers
- Began formwork for pier and caps


Roadway Construction (DBC, Inc):

- Continued installation of storm drainage system at various locations
- Continued construction of remaining Stormwater Management Basin: SWM 1
- Continued monitoring advanced settlement from surcharges, completed at several locations.
- Continued construction of ramps at north end of project
- Continued grading operations at Dominion Lakes Blvd and Ramp G and Ramp H

Major Subcontractors

- **Bissette Construction Corp**
 - Continued installation of storm drain systems south of Elizabeth River at various locations
- **Hampton Roads Utility**
 - Continued final service tie-ins
- **US Wick Drains**
 - Not on site this month
- **Roche Brothers**
 - Continued installing MSE Wall Panels at B610, B611, B612 and B613 Abutments.
- **Virginia Sign and Lighting**
 - Completed concrete placement for signal pole foundations at Great Bridge Blvd.
 - Completed installation of new permanent traffic signals at Cedar Rd and Access Rd intersection.
- **Virginia Paving Co**
 - Completed paving of Ramp G, Ramp H, and Dominion Lakes Blvd. intersection
- **Uretek ICR Mid- Atlantic**
 - Continued construction of Soil Nail Walls at Ramp P, Ramp J, and Ramp L.
- **Reliance Concrete Contractors**
 - Continued placing concrete for leveling course and moment slab at MSE Walls 12 & 15

- Completed placing concrete for curb at Dominion Lakes Blvd, Chesapeake Schools proposed parking lot and bus exit
- Continued placing concrete for curb on Ramp N, Jones Lane cul-de-sac, and Ramp I
- **Hylton Builders Inc**
 - Completed construction of triple box culvert on Dominion Blvd
- **Lasting Coastline Inc**
 - Completed setting concrete barrier on MSE Wall 17
 - Continued setting concrete barrier on MSE Wall 15

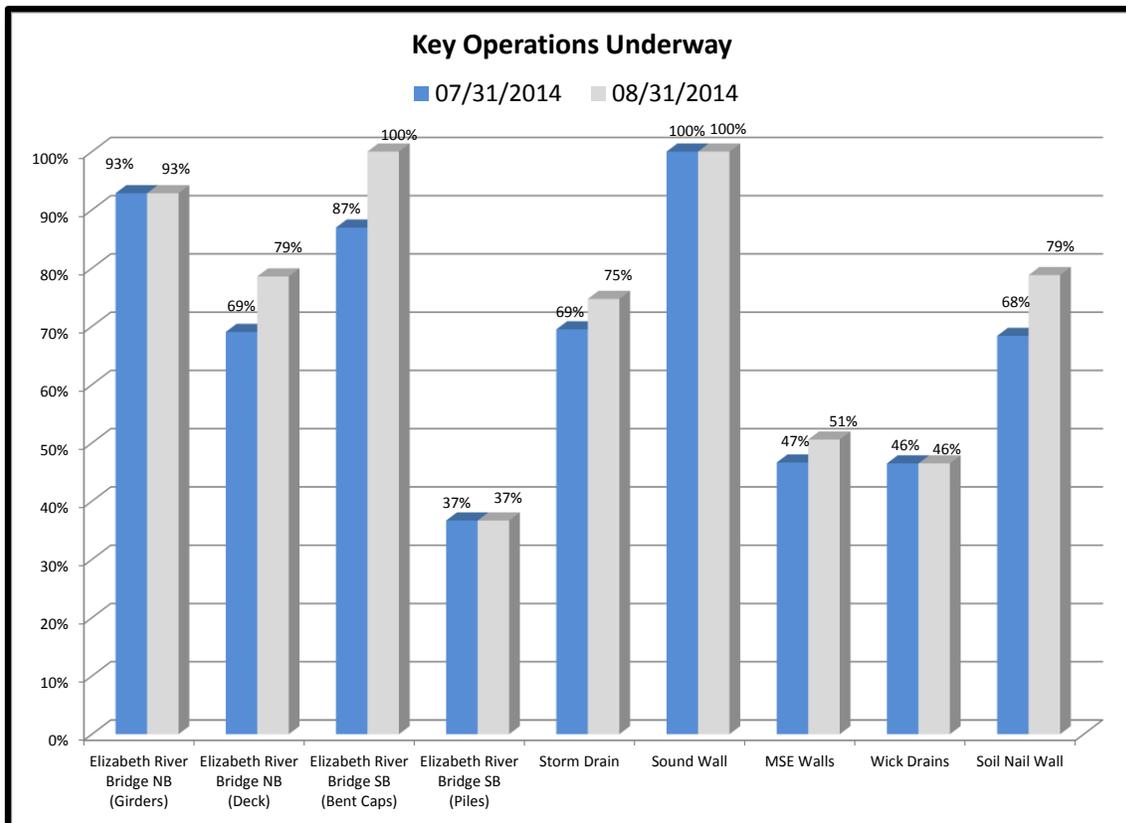


Project Key Operation Status as of 08/31/2014

Key Operations Completed	Month Completed
Elizabeth River Bridge NB (Bent Caps)	Aug-13
Elizabeth River Bridge NB (Piles)	Sep-13
Open Detour A	Oct-13
Elizabeth River Bridge NB (River Footings)	Nov-13
Opened relocated Dom Blvd. at Cedar Road	Jan-14
Partially opened Access A and Access AA	Mar-14
Opened Blake Street	Apr-14
Completed Setting Navigation Span Beams	May-14
Opened permanent intersection for Access A/AA at Cedar Rd.	Jun-14
Completed Stage 1 Post-Tensioning for B609 spliced Girders	Jul-14
Completed Dominion Lakes Blvd. entrance	Aug-14

MAINTENANCE OF TRAFFIC

Lane Closures

- Various temporary lane closures throughout project including night-time closures to minimize impacts to motorists
- Detour A is in place to divert Dominion Blvd traffic and enable start of B608 construction

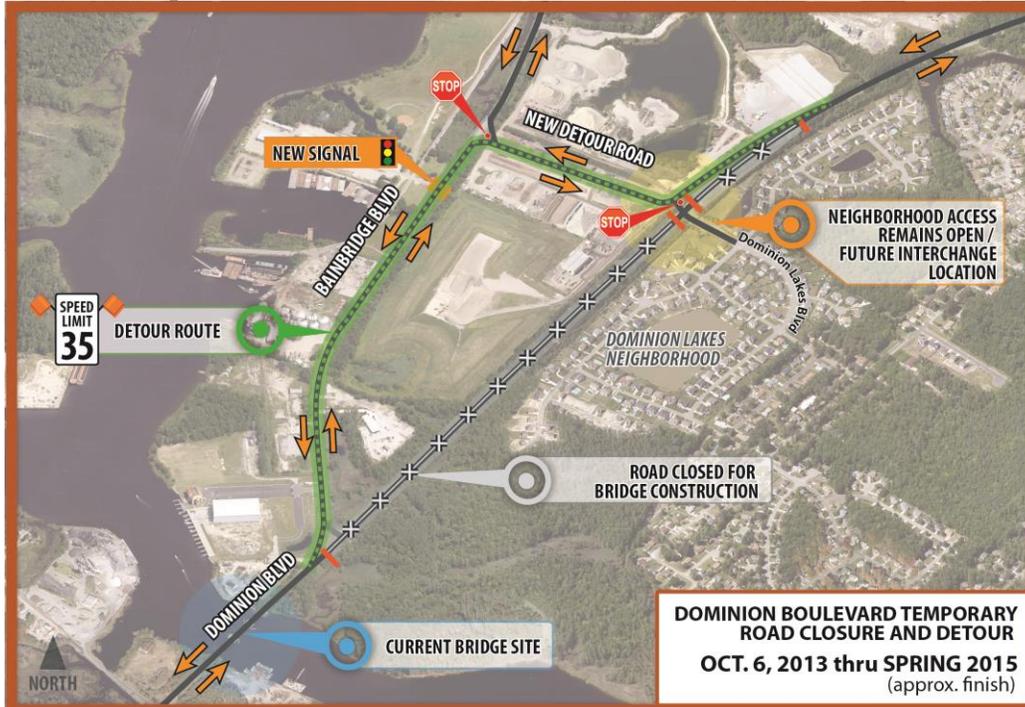

Detour A (Relocated Bainbridge) completed:
(Arrows show temp. traffic pattern for Dominion Blvd.)

- Ramp P (Rte. 168 N Exit 15B to Dominion Blvd S) remains closed for road widening per plans. Traffic is being detoured using a double loop at Exit 1 (Rte 464) to Rte 168 S Exit 15B.



Detour Route for Ramp P Closure

- Traffic on Dominion Blvd. remains shifted slightly to a temporary roadway at Moses Grandy to enable construction of B612 and B613 to begin.
- Opened Dominion Lakes Blvd. and Dominion Blvd. intersection on August 29th, 2014

ANTICIPATED WORK PLANNED FOR NEXT MONTH (09/01/14 – 09/30/14)**DBC Joint Venture**

- B609 (Dominion Blvd. NB Bridge over Elizabeth River)
 - Continue installing deck formwork south of the river and continue placing concrete for the deck.
 - Complete forming and concrete placement for the navigation span
 - Complete setting girders for span 1.
 - Begin preparations for second phase post tensioning of navigation span girders
- B608 (Dominion Blvd. SB Bridge over Elizabeth River)
 - Continue concrete placements for bent caps, columns and footings
 - Continue installing girders at bent caps and begin deck construction
- B616 (Dom. Blvd./Rte. 168 SB Ramp over Great Bridge Blvd. to I-64 Ramp)
 - Complete concrete placements for parapet walls
- B610 and B611 (Dominion Blvd SB and NB over relocated Bainbridge Blvd)
 - Continue forming deck in preparation for concrete placement
- B612 and B613 (Dominion Blvd SB and NB over Cedar Rd/ Moses Grandy)
 - Continue concrete placement for pier footers, columns and caps
- Continue installation of storm drainage systems at various locations
- Continue construction of new Dominion Blvd. including MSE walls for ramps at various locations
- Begin placing cement treated aggregate and preparations for asphalt on Dominion Blvd main line

Hampton Roads Utilities

- Complete tie-ins for water services to new relocated water lines

Roche Brothers

- Continue installation of MSE Walls at B609, B612 and B613 Abutments

Reliance Concrete Contractors Inc

- Continue installing moment slab and leveling course at various MSE Walls
- Continue placing curb at various locations

Virginia Sign and Lighting

- Begin installing temporary and permanent signals at Great Bridge Blvd.
- Begin installing lighting system on B609

Virginia Paving

- Continue placing asphalt for permanent ramps and roadway at various locations.



Change Orders

Requested Change Orders			
Change Order Number	Scope	Exposure from Change Orders (\$)	Expenditures from Change Orders (\$)
01	Add Flaggers & Portable Changeable Message Signs		\$91,071.25
02	Replace Porous fill with strip drains at MSE Walls		(\$1,444,802.94)
03	Raise B608 & B609 Bridge Footings		(\$810,117.50)
04	Add'l electric service per plan Rev. 1/18/2013		\$139,651.02
05	Add #57 stone to the contract		\$851,600.00
06	Add Trainees to the contract		\$45,000.00
07	2" HDPE Conduit - Bored		\$25,747.68
08	8" Sanitary Force Main Under Wetlands		\$22,601.25
09	B609 Pier 14 Pile Modif.		\$831,940.75
10	Temp. Signal at Bainbridge and Sta. 55+50		\$73,977.55
11	Type D Removable Pavement Markings for Concrete		\$47,400.00
12	Removal of Concrete Barriers (\$12.50/LF)		\$6,000.00
13	Ramp K/MSE Wall 22 Wick Drains		\$305,633.61
14	Demolition/Removal of Existing Sound Wall		\$72,643.23
15	Disposal of Unsuitable Material (base on 140,000 cy)		\$6,025,600.00
16	MSE Walls at Bridge Abutments B610-B615		(\$239,207.30)
17	Delete Aesthetic Treatment		(\$1,838,302.58)
18	4 inch water meters at Great Bridge & Cedar		\$10,772.06
19	Relocation of the Pressure Sensor Telemetry Cabinet; 8/29/2013		\$23,457.35
20	Water Meter Vault at DR-1J50-1		\$11,157.98
21	Anti-Graffiti Paint - 8/26 Rec'd DBC's Revised Scope	\$219,823.36	
22	16 inch Waterline Repairs at Bainbridge	\$18,116.70	
23	Temp. Street lights at Cedar/Dominion Blvd	16,717.73	
24	Soil Nail Wall	\$247,184.50	
25	12" x 12" x 8" Junction Boxes	\$36,026.55	
26	Installation of Leak Detectors Water/Sewer Casings	\$47,359.48	
27	New High Mast Light Assembly	\$60,454.18	
28	Grass Cutting	\$152,556.48	
29	Missing Pay Items: RW2, RW3, Impact Attenuators	\$361,862.19	
30	Replace MC-3B Asphalt Curb with Conc. Curb (VEP 07)	(\$39,402.03)	
31	Remove Existing Sign Structures	\$6,192.66	
32	GPS As-Builts of Utilities	\$84,527.20	
33	Plan Revision No. 14 Additional Work	\$476,877.44	
34	Soil Nail Walls - Additional Work	\$141,766.40	
(TBD)	VDOT VMS Sign Removal/Reinstall	\$47,883.33	
(TBD)	Structure 32-10 Add.	\$8,929.89	
(TBD)	Plan Rev. No. 8 8" PVC Sewer	\$16,808.21	
(TBD)	Removal of Underground Water Storage Tanks	\$15,065.49	
(TBD)	Installation of Verizon Vaults and Pedestals	\$64,255.85	
(TBD)	24" x 6" Reducer for Additional Fire Hydrant	\$4,172.63	
(TBD)	Obstruction at 18" Jack and Bore	\$67,865.38	
(TBD)	Connection of Existing Sewer Laterals to New, Relocated Sewer	\$18,061.62	
(TBD)	Additional Work Associated with Revision 10	\$6,570.40	
(TBD)	Obstructions between Str. 23N-1 and 23N-2	\$23,114.87	
(TBD)	Additional Restrained Waterline	\$10,793.22	
(TBD)	CCW Type D Lighting Control Cabinets	\$150,513.73	
(TBD)	Plan Revision No 12 Added Wick Drains/Survey	\$35,593.37	
(TBD)	Temporary Drainage at Detour A	\$17,634.06	
(TBD)	Waterline Joint Restraint at Great Bridge Blvd.	\$4,701.38	
(TBD)	VMS Conductor Cable	\$19,502.00	
(TBD)	Remove/Salvage Existing Signal Equipment	\$39,115.32	
(TBD)	Plan Revision No. 13 Additional Work	\$19,456.14	
(TBD)	24" Waterline tie-in delays at Cedar Road	\$8,114.82	
(TBD)	B609 Pier No. 3-8 Rebar Changes to Caps	\$21,753.35	
(TBD)	Plan Revision No. 15 Additional Work	\$29,528.83	
(TBD)	VPDES Permit Re-application and Maintenance Fee	\$16,054.35	
(TBD)	Wireless System Coaxial Cable for Traffic Signals	\$44,584.98	
(TBD)	Replace existing junction boxes	\$15,192.04	
(TBD)	Optional Tolling Interoperability Functionality	\$310,626.13	
(TBD)	Remove Existing Sign Structures D704 & D14	\$8,214.60	
(TBD)	MSE Wall Redesign	\$335,851.60	
NA	RESCINDED: Sewer Force Main Offset Blake/GBB		\$0.00
NA	RESCINDED: Utilities at 18" HRSD (Sta. 22+50 to Sta. 23+00)		\$0.00
NA	RESCINDED: Installation of F-Shaped Conc. Barrier		\$0.00
NA	RESCINDED: Per RFI 191 - Storm Drain		\$0.00
NA	RESCINDED: Relocate HRSD Leak Detector Conflict		\$0.00
NA	RESCINDED: Storm Drain Adjustments		\$0.00
TOTAL		\$3,190,020.43	\$4,251,823.41
			Contract Addition



Unit Price Item Quantities – Projected and Actual Overruns

Unit Price Item Quantity Overruns (Projected Quantity Overruns)					
Item Number	Description	Projected Quantity Overrun	Units	Unit Price	Projected Cost Overrun
111	CLEARING AND GRUBBING	28.16	AC	\$ 7,700.00	\$ 216,832.00
120	REGULAR EXCAVATION	39543.59	CY	\$ 29.00	\$ 1,146,764.11
212	MINOR STRUCTURE EXCAVATION BOX CULVERT	1280	CY	\$ 35.00	\$ 44,800.00
505	BEDDING MATERIAL AGGR. NO. 25 OR 26	2700	TON	\$ 78.50	\$ 211,950.00
27500	GEOTEXTILE FABRIC	21010	SY	\$ 6.70	\$ 140,767.00
525	CONCRETE CLASS A3 MISC.	59	CY	\$ 2,913.26	\$ 171,882.34
27550	STORMWATER MANAGEMENT DRAINAGE STRUCTURE SWM-1	22	LF	\$ 6,232.87	\$ 137,123.14
9148	EROSION CONTROL STONE (CLASS A1), EC-1	978	SY	\$ 111.98	\$ 109,516.44
9150	EROSION CONTROL STONE (CLASS I), EC-1	3500	SY	\$ 147.48	\$ 516,180.00
85003	UNDERCUT EXC @ TWICE REG EXC	33713	CY	\$ 50.00	\$ 1,685,650.00
10636	ASPHALT CONCRETE TY. SM-9.5D	1750	TON	\$ 75.00	\$ 131,250.00
22643	FENCE FE-CL	3800	LF	\$ 12.19	\$ 46,322.00
27321	PROTECTIVE COVERING EC-2	64583	SY	\$ 1.35	\$ 87,187.05
13570	NS RETAINING WALL MSE	5000	SF	\$ 56.37	\$ 281,850.00
13570	NS RETAINING WALL TEMPORARY	7100	SF	\$ 30.00	\$ 213,000.00
2093	NS PRE-DRILLING OF WICK DRAINS	851,250.73	LF	\$ 1.85	\$ 1,574,813.84
515	TEMPORARY SHEET PILING	10000	SF	\$ 25.00	\$ 250,000.00
10065	AGGR. MATL. NO. 1	1000	TON	\$ 35.91	\$ 35,910.00
24283	POLICE PATROL	1200	HR	\$ 42.40	\$ 50,880.00
56052	BORED CONDUIT 4"	31580	LF	\$ 32.90	\$ 1,038,982.00
56053	2" PVC CONDUIT	36330	LF	\$ 2.25	\$ 81,742.50
56055	4" PVC CONDUIT	12393.04	LF	\$ 4.81	\$ 59,610.52
64424	PRESTR. CONCRETE PILES 24"	400.6	LF	\$ 80.00	\$ 32,048.00
64868	DRIVING TEST FOR 24" PRESTR. CONC. PILE	237	LF	\$ 150.00	\$ 35,550.00
64416	PRESTR. CONCRETE PILES 16"	770.77	LF	\$ 65.00	\$ 50,100.05
40081	8" DI WATER MAIN	1220	LF	\$ 47.74	\$ 58,242.80
42080	8" PVC SAN PIPE	269.35	LF	\$ 157.15	\$ 42,328.35
44301	NS FURNISH and INSTALL 24" LINSTOP	2	EA	\$ 73,658.52	\$ 147,317.04
38900	NS SALT MARSH CORDGRASS, 2" PLUG	18320	EA	\$ 1.95	\$ 35,724.00
42080	8" DI SAN PIPE	365	LF	\$ 93.51	\$ 34,131.15
	Miscellaneous				\$ 735,199.18
	Total				\$ 9,403,653.52




Unit Price Item Quantity Overruns (Actual Quantity Overruns)					
Item Number	Description	Actual Quantity Overrun	Units	Unit Price	Actual Cost Overrun
111	CLEARING AND GRUBBING	28.16	AC	\$ 7,700.00	\$ 216,832.00
120	REGULAR EXCAVATION	38219.9	CY	\$ 29.00	\$ 1,108,377.10
212	MINOR STRUCTURE EXCAVATION BOX CULVERT	1182.83	CY	\$ 35.00	\$ 41,399.05
505	BEDDING MATERIAL AGGR. NO. 25 OR 26	2509.3	TON	\$ 78.50	\$ 196,980.05
27500	GEOTEXTILE FABRIC	20974.42	SY	\$ 6.70	\$ 140,528.61
525	CONCRETE CLASS A3 MISC.	42.2	CY	\$ 2,913.26	\$ 122,939.57
1482	48" CONC. PIPE	102.9	LF	\$ 208.18	\$ 21,421.72
27550	STORMWATER MANAGEMENT DRAINAGE STRUCTURE SWM-1	13.3	LF	\$ 6,232.87	\$ 82,897.17
9148	EROSION CONTROL STONE (CLASS A1), EC-1	750.86	SY	\$ 111.98	\$ 84,081.30
9150	EROSION CONTROL STONE (CLASS I), EC-1	3006.23	SY	\$ 147.48	\$ 443,358.80
85003	UNDERCUT EXC @ TWICE REG EXC	33649.38	CY	\$ 50.00	\$ 1,682,469.00
10417	TACK COAT	1543.27	GAL	\$ 15.90	\$ 24,537.99
24602	REMOVE EXISTING (FENCE)	6419	LF	\$ 3.18	\$ 20,412.42
51910	SAW CUT	5690	LF	\$ 2.07	\$ 11,778.30
27321	PROTECTIVE COVERING EC-2	57206.82	SY	\$ 1.35	\$ 77,229.21
13570	NS RETAINING WALL TEMPORARY	5736.1	SF	\$ 30.00	\$ 172,083.00
2093	NS PRE-DRILLING OF WICK DRAINS	622209	LF	\$ 1.85	\$ 1,151,086.65
64808	DRIVING TEST FOR PRESTRESSED CONCRETE PILES 12"	464	LF	\$ 55.00	\$ 25,520.00
27410	CHECK DAM, ROCK-TYPE I	31	EA	\$ 370.67	\$ 11,490.77
27526	TURBIDITY CURTAIN, IMPERVIOUS	1226	LF	\$ 18.02	\$ 22,092.52
515	TEMPORARY SHEET PILING	6106.43	SF	\$ 25.00	\$ 152,660.75
56052	BORED CONDUIT 4"	31261	LF	\$ 32.90	\$ 1,028,486.90
56200	TRENCH EXCAVATION ECI-1	2846	LF	\$ 4.59	\$ 13,063.14
64101	DYNAMIC PILE TEST (FRICTION PILES)	4.33	EA	\$ 3,000.00	\$ 12,990.00
64416	PRESTR. CONCRETE PILES 16"	338	LF	\$ 65.00	\$ 21,970.00
64424	PRESTR. CONCRETE PILES 24"	400.6	LF	\$ 80.00	\$ 32,048.00
64868	DRIVING TEST FOR 24" PRESTR. CONC. PILE	237	LF	\$ 150.00	\$ 35,550.00
64416	PRESTR. CONCRETE PILES 16"	335	LF	\$ 60.00	\$ 20,100.00
66921	NS BRIDGE SUB-STRUCTURE PRE-BORING (16" PRESTRESSED CONC)	460	LF	\$ 25.00	\$ 11,500.00
61704	CORROSION RESISTANT REINF.STEEL (Plan Quantity)	5690	LB	\$ 1.80	\$ 10,242.00
40061	6" DI WATER MAIN	438	LF	\$ 42.31	\$ 18,531.78
40081	8" DI WATER MAIN	740.84	LF	\$ 47.74	\$ 35,367.70
40121	12" DI WATER MAIN	202	LF	\$ 83.54	\$ 16,875.08
40161	16" DI WATER MAIN	147	LF	\$ 86.80	\$ 12,759.60
40408	18" BEND	4	EA	\$ 2,820.91	\$ 11,283.64
40992	NS 8" BEND	22	EA	\$ 515.36	\$ 11,337.92
40992	NS 4" BEND	5	EA	\$ 2,766.65	\$ 13,833.25
41982	NS 4" OFFSET	5	EA	\$ 4,705.65	\$ 23,528.25
44301	NS FURNISH and INSTALL 24" LINSTOP	2	EA	\$ 73,658.52	\$ 147,317.04
38900	NS SALTMARSH CORDGRASS, 2" PLUG	18000	EA	\$ 1.95	\$ 35,100.00
40992	3" BEND	5	EA	\$ 2,169.93	\$ 10,849.65
42080	8" DI SAN PIPE	365	LF	\$ 93.51	\$ 34,131.15
40006	2" WATER SERVICE LINE	186	LF	\$ 54.25	\$ 10,090.50
					\$ 299,932.12
					\$ 7,677,063.72


Summary Unit Price Item Overruns:

Current Projected Quantity Overruns	\$ 9,403,653.52
Actual Quantity Overruns	<u>\$ 7,677,063.72</u>
Net Projected Quantity Overruns	\$ 1,726,589.80

Submittals and RFI Status

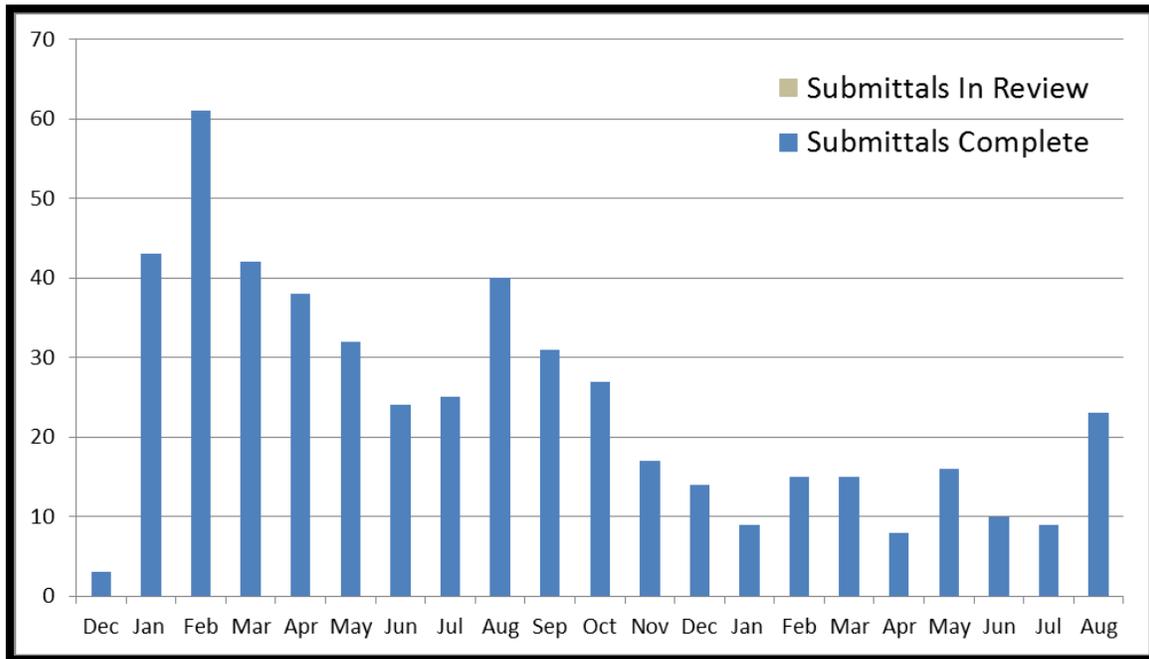

Total Number of Submittals = 502 ; Number of Submittals in review = 0 ;

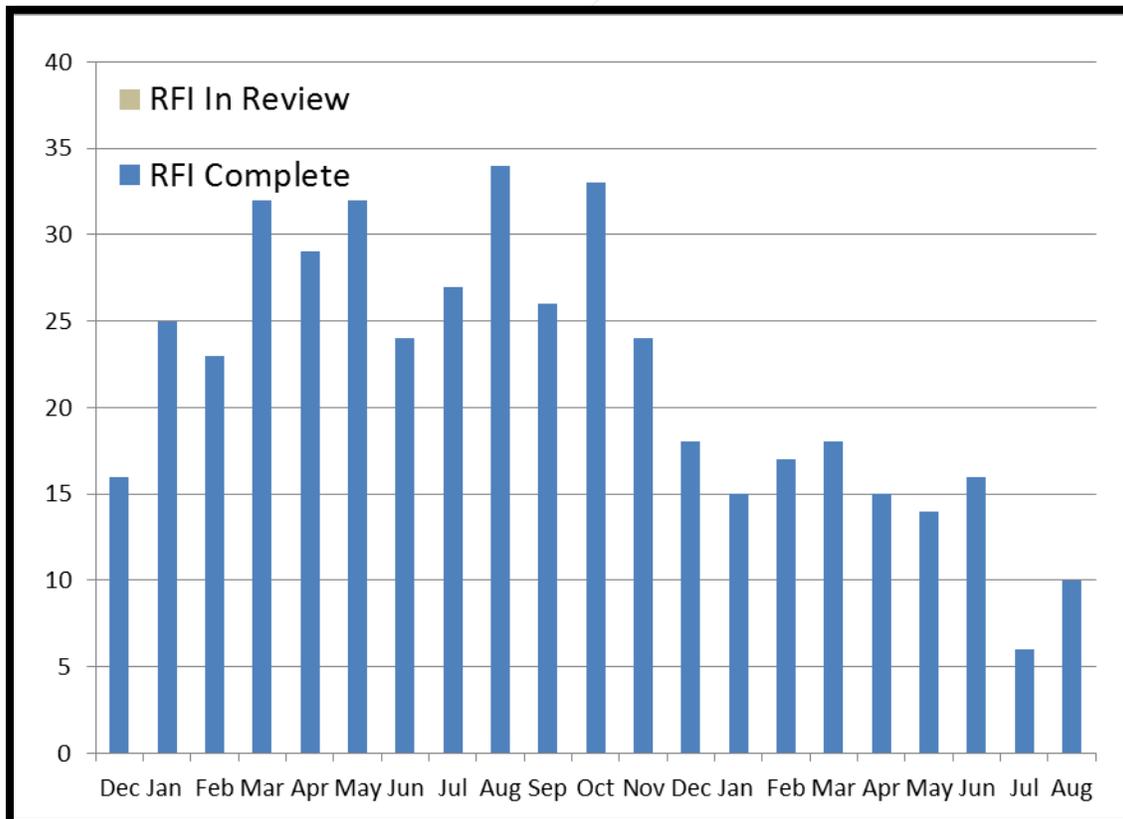

Total Number of RFI = 454 ; Number of RFI in review =0;

SCHEDULE

- The Contractor submitted CPM schedule Update 14 with a data date of 08/25/2014. Update 14 has the projected completion on March 31, 2017 which meets the contract completion requirement of April 1, 2017. The following chart summarized the current milestones in DBC's schedule and a comparison of projected Early Finish/Late Finish dates with the July 2014 CPM schedule update

Milestones

Activity ID	Activity Name	Status	July 2014 Update 13		August 2014 Update 14		Actual Finish
			Early Finish	Late Finish	Early Finish	Late Finish	
1MS1010	Access Road C Complete	Not Completed	12/18/2014	2/9/2015	1/21/2015	2/9/2015	
1MS1020	Bridge B-616 Complete	Not Completed	8/8/2014	8/20/2015	8/28/2014	8/20/2015	
1MS1030	Great Bridge Blvd Through Ramps complete	Not Completed	4/22/2016	3/31/2017	5/27/2016	3/31/2017	
1MS1040	B615 Complete	Not Completed	2/12/2016	3/31/2017	3/25/2016	3/31/2017	
1MS1045	B614 Complete	Not Completed	2/12/2016	3/31/2017	3/25/2016	3/31/2017	
1MS1110	Ramp N Complete	Not Completed	10/8/2014	8/20/2015	11/6/2014	8/20/2015	
1MS1120	Ramps P & J Complete	Not Completed	11/13/2014	8/20/2015	12/11/2014	8/20/2015	
1MS1130	Ramp I Complete	Not Completed	9/2/2014	9/30/2015	9/29/2014	9/30/2015	
1MS1140	Ramp M Complete	Not Completed	10/27/2014	9/30/2015	11/4/2014	9/30/2015	
1MS1150	Shift Traffic to Phase 2 (Ramps I, L, M, P & under K Complete)	Not Completed	1/16/2015	8/20/2015	2/27/2015	8/20/2015	
2MS1110	B-609 Complete	Not Completed	2/5/2015	2/9/2015	2/9/2015	2/9/2015	
2MS1120	B-610 Complete	Not Completed	1/26/2015	3/31/2017	1/30/2015	3/31/2017	
2MS1130	B-611 Complete	Not Completed	11/24/2014	2/9/2015	11/13/2014	2/9/2015	
2MS1140	Shift Traffic to B-609	Not Completed	2/5/2015	2/9/2015	2/9/2015	2/9/2015	
2MS1150	Ramp H Complete	Not Completed	1/26/2015	2/9/2015	1/30/2015	2/9/2015	
2MS1160	Ramp G Complete	Not Completed	12/25/2014	2/9/2015	1/7/2015	2/9/2015	
2MS1170	B-608 Complete	Not Completed	3/31/2017	3/31/2017	3/31/2017	3/31/2017	
2MS1180	Close Ramps G, H, Dominion Lakes & DetourA	Not Completed	2/5/2015	11/21/2016	2/9/2015	11/21/2016	
2MS1190	Ramp F & Bainbridge Blvd. Complete	Not Completed	7/8/2016	3/31/2017	7/29/2016	3/31/2017	
334EW1170	Ramp G, to Box Culvert Complete	Not Completed	9/4/2014	2/9/2015	9/25/2014	2/9/2015	
361EW1200	Station 361 to B614/B615 Complete SB	Not Completed	7/8/2016	3/31/2017	7/29/2016	3/31/2017	
361EW1480	Station 361 to B614/B615 Complete NB	Not Completed	2/12/2016	3/31/2017	3/25/2016	3/31/2017	
361EW1650	609 Abutment B through Ramp H Complete	Not Completed	1/26/2015	2/9/2015	1/30/2015	2/9/2015	
3MS1011	Ramps C & D Available for B-609 traffic	Not Completed	2/3/2015	7/27/2015	3/9/2015	7/27/2015	
3MS1020	Phase 3 Complete	Not Completed	8/22/2016	3/31/2017	9/21/2016	3/31/2017	
3MS1030	Cedar Road/Moses Grandy Complete	Not Completed	8/25/2015	3/31/2017	9/11/2015	3/31/2017	
612-M9000	B612 Complete	Not Completed	8/25/2015	3/30/2017	9/10/2015	3/30/2017	
613-M9000	B613 Complete	Not Completed	7/8/2015	3/30/2017	7/30/2015	3/30/2017	
GBMS1050	Great Bridge Blvd Phase 1 Complete	Not Completed	11/28/2014	8/20/2015	12/31/2014	8/20/2015	
MS0020	Contract Completion	Not Completed	3/31/2017	3/31/2017	3/31/2017	3/31/2017	
MS1020	Early Completion	Not Completed	9/22/2016	9/22/2016	9/22/2016	9/22/2016	
RKEW4150	Ramp K Complete	Not Completed	8/28/2014	8/20/2015	9/25/2014	8/20/2015	
RLEW1080	Place Traffic on completed Ramps R & L	Not Completed	8/22/2016	3/31/2017	9/21/2016	3/31/2017	
RLEW1230	Ramp L Under K Complete	Not Completed	8/18/2014	8/20/2015	9/15/2014	8/20/2015	
ROUT1090	Ramp O Complete	Not Completed	1/16/2015	8/20/2015	2/27/2015	8/20/2015	
AHEW1080	Access Road H Complete	Completed					7/26/2013
609-D1010	Clearing and Access Complete	Completed					3/22/2013
RKUT4110	Ramp K Utilities Complete	Completed					6/10/2013
RNEW1000	Ramp N Ground Improvements (Tied to RKEW4050)	Completed					1/10/2014
2MS1100	Shift Traffic To Detour A	Completed					10/6/2013
3MS1000	Traffic to Temp Ramp A & B	Completed					1/25/2014

Reviewed by:

Mike Prezioso, PE, CCM, MBP

cc: Kevin Lundgren, PE, City of Chesapeake
Leon Malczewski, CCM, MBP

Attachement: Progress Photos



08/06/2014 Construction of B610/B611 over Dominion Lakes Dr.



08/27/2014 Construction of B610/B611 over Dominion Lakes Dr.



08/06/2014 Construction of B612 & B613 Pier 2 (Cedar Rd.)



08/27/2014 Construction of B612 & B613 Pier 2 (Cedar Rd.)



07/08/2014 Storm Water Management Pond 1 Excavation Looking South East



08/27/2014 Storm Water Management Pond 1 Excavation Looking South East



08/06/2014 B609 Bridge Deck - Looking South



08/27/2014 B609 Bridge Deck alongside B608 Bridge Girders - Looking South



08/27/2014 B609 Main Span Under Construction NB over Eliz. River Southern Bank



08/27/2014 Construction of B608/B609 shared Fender System



09/5/2014 Construction Soil Nail Wall 24



08/27/2014 Completed paving of Dominion Lakes Dr. with Ramps G & H
